

Mission Hill MS | Update

SANTA CRUZ CITY SCHOOLS | PLANNING REVIEW COMMITTEE – 03 JUNE 2021

BARTOS
ARCHITECTURE

COLLABORATION
ADVOCACY
RESEARCH
EDUCATION

03 June 2021

Bond Committee Update

Agenda

01

Completed Projects

02

Present Projects

03

Imminent Projects

04

Future Projects

05

Priorities and implementation

Bond Committee Update

Past | Complete

- ✓ Front Landscape Improvements.
- ✓ Front Shade Structure and Monument Sign.
- ✓ Accessible Student Restroom
- ✓ Roofing Phase 1: Main Building
- ✓ Locker Room Improvements
- ✓ Mod Phase 1: Permanent Partitions
- ✓ Fire Sprinkler Line Replacement
- ✓ Site Security Fencing Complete
- ✓ Site Data Improvements Complete
- ✓ Site Handrail Replacement Complete
- ✓ Auditorium Improvements (partial completion)

Present

- Playfield
- Gymnasium roofing (to be ok'd in this meeting)
- New ornamental entry gate (end of summer)
- Electrical Power / Switchgear (in progress)

Next Summer

- Exterior Envelope

Future

- New Building



Upcoming Scope

- ✓ New Ceiling Tiles
- ✓ New Lighting

Envelope Mod Scope

- New Windows
- New Shades
- New Stage Curtain
- New Acoustic Panels
- New Paint

- ✓ New Floor


Remainder to be completed with “envelope” project in summer 2022

Auditorium Improvements

Bond Committee Update : Ms Crocetti's Art Students !




Bond Committee Update : Ms Crocetti's Art Students !




Bond Committee Update



New Entry Gate on King Street

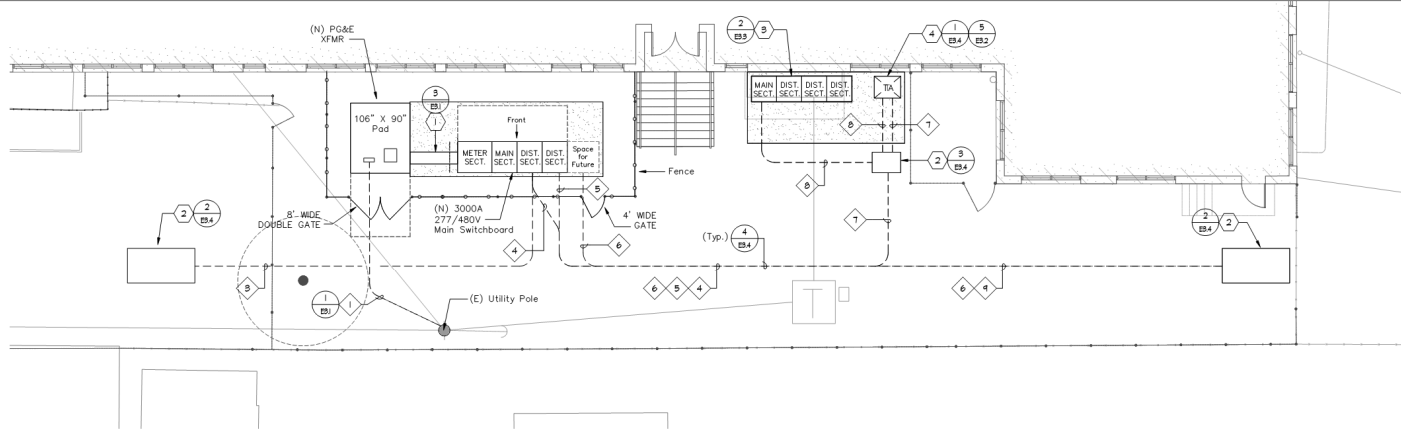

1 Enlarged Switchgear Plan
E1.2 SCALE: 1" = 1/8'-0"

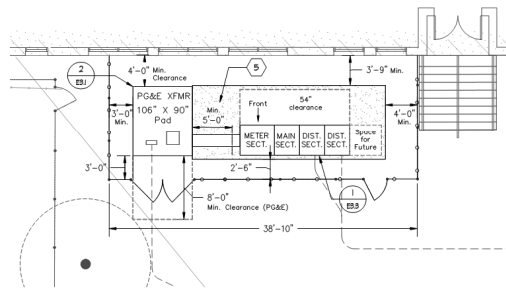

2 Electrical Switchgear Dimensions
E1.2 SCALE: 1" = 1/8'-0"

Electrical Switchgear: Site Power Upgrade



Electrical Switchgear: Site Power Upgrade



Fields: Chris Garcia

03 June 2021

collaboration | advocacy | research | education | sustainability

BARTOS
ARCHITECTURE

Master Plan - Revised

Current Multi-phase master plan



	Current Bond Resource	\$17,648,740	\$18,399,904
01 Landscape Shelter Access	\$1,298,161	\$1,298,161	
02 Roofing Phase 1: Main	\$1,618,192	\$1,618,192	
03 Exterior Site Imp. (Fencing)	\$100,000	\$100,000	
04 Gym Phase 1: Locker Rooms	\$158,912	\$158,912	
05 Mod Phase 1: incl. Partitions	\$322,216	\$322,216	
06 Data Infrastructure Improvements	\$575,782	\$575,782	
07 Card access security system	\$182,276	\$182,276	
08 Mod Ph 2: incl. Auditorium	\$300,000	\$300,000	
09 Replace existing Playfields	\$3,000,000	\$3,000,000	
10 Utility Infrastructure (incl power)	\$1,000,000	\$1,000,000	
11 Mod Ph 3: Main Building (Envelope)	\$2,000,000	\$1,417,480	
		Gymnasium Roofing	\$750,000
12 New Modular CR Building	\$6,424,679	\$6,424,679	
Multi Project Overhead	\$ 952,206	\$952,206	
Total	\$17,648,740	\$18,399,904	

Committed | Complete

Confirmation Required:

- Add Gym Roofing Project
- Reduce scope of Mod Phase 3 Main Building Envelope

Funding Dependent Projects/Priorities

- Gymnasium Phase 2 – Reconfiguration and improvements
- Site Improvements (portable removal)
- Some components of Envelope project (alternate bids)

Bond Committee Update

Agenda

01

Completed Projects

02

Present Projects

03

Imminent Projects

04

Future Projects

05

Priorities and implementation

Bond Committee Update

End

03 June 2021
