# ARCHITECTURE & PLANNING

## Measure B Bay View Elementary Campus Updates



OCTOBER 08, 2020

# AGENDA

Campus Master Plan Budget Overview Modernization Future Projects Budget Review Next Steps













FUTURE PROJECTS



#### BAY VIEW ELEMENTARY SCHOOL – MEASURE B



PROJECT	START	COMPLETE	PROJECT BUDGET
MULTI-PROJECT OVERHEAD	ONGOING	ONGOING	\$25,000
RE-ROOFING	COMPLETE	COMPLETE	\$925,529
WPENS RELOCATION & SITE WORK	CANCELLED	CANCELLED	\$41,858
NEW KINDERGARTEN BUILDING & SITE WORK	FUTURE BOND	FUTURE BOND	\$92,477
NEW CLASSROOM BUILDING & SITE WORK	COMPLETE	COMPLETE	\$4,150,000
CLASSROOM MODERNIZATION (PHASE 1)	04/01/2020	11/06/2020	\$6,000,442
CLASSROOM MODERNIZATION (PHASE 2)	04/01/2020	12/31/2020	\$225,518
PORTABLE DEMOLITION & SITE WORK	06/15/2021	08/23/2021	\$83,213
SITE INFRASTRUCTURE			\$10,984
CARD ACCESS SECURITY SYSTEM	06/10/2019	08/21/2021	\$190,000
DATA INFRASTRUCTURE IMPROVEMENTS	06/10/2019	08/21/2021	\$453,169
		TOTAL	\$12,198,190

OVERALL SITE BUDGET: \$12,384,192



#### CAMPUS MODERNIZATION – PHASING





#### CAMPUS MODERNIZATION – ADMINISTRATION BUILDING





RENDERED FRONT ENTRANCE TO BAY VIEW ELEMENTARY SCHOOL



Bay View Elementary School Bond Projects

#### NEW FRONT ENTRANCE TO THE CAMPUS



#### CAMPUS MODERNIZATION – ADMINISTRATION BUILDING


















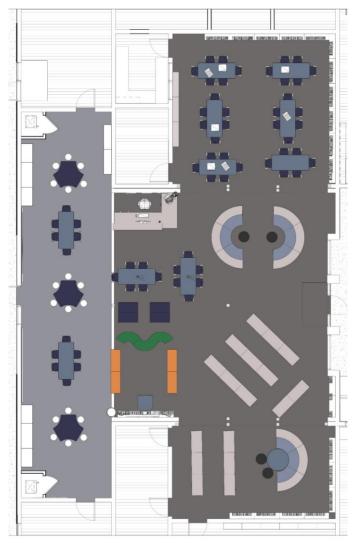















LIBRARY RENDERINGS









LIBRARY RENDERINGS





#### CAMPUS MODERNIZATION – CLASSROOMS



PHOTO OF ONGOING CONSTRUCTION

MADI



#### CAMPUS MODERNIZATION – CLASSROOMS





#### PHOTO OF CONSTRUCTED CLASSROOMS



#### CAMPUS MODERNIZATION – CLASSROOMS








#### ADDITIONAL CLASSROOM FURNISHINGS



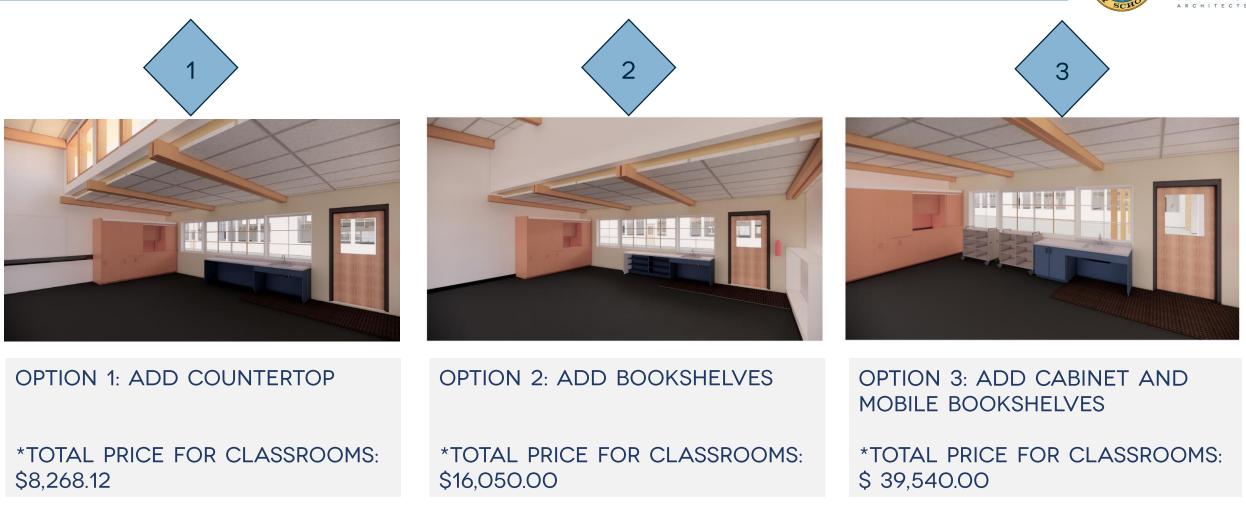




Bay View Elementary School Bond Projects

\*TOTAL OF 10 CLASSROOMS

#### CAMPUS MODERNIZATION – NEW LANDSCAPING



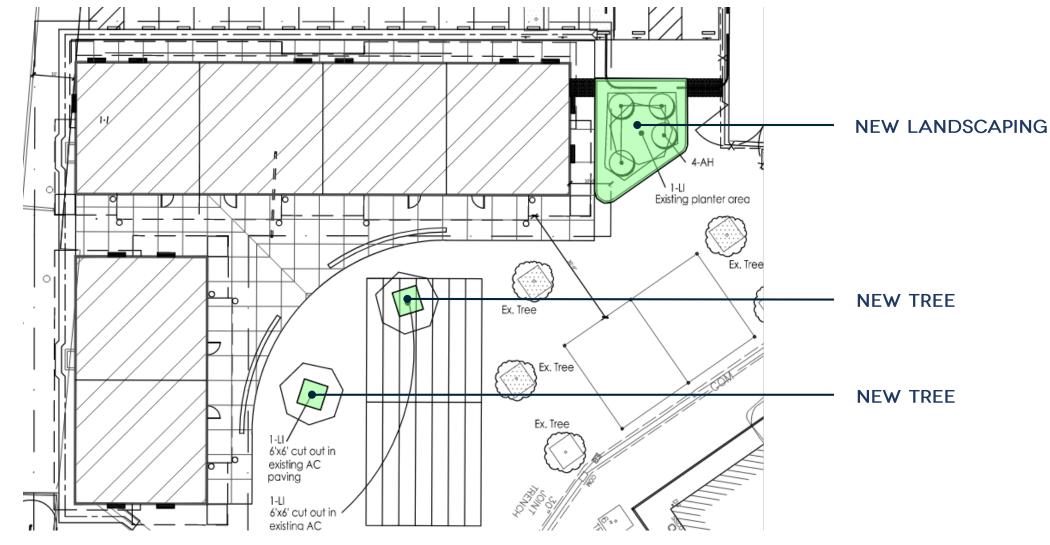



#### CAMPUS MODERNIZATION – FUTURE PROJECTS









POTENTIAL PROJECTS	ESTIMATES
OPTION 1 FURNITURE	\$8,268.12
OPTION 2 FURNITURE	\$16,050.00
OPTION 3 FURNITURE	\$39,540.00
NEW SHADE STRUCTURE	\$65,000.00
BALL WALL	\$30,000.00



#### BAY VIEW ELEMENTARY SCHOOL – MEASURE B



PROJECT	START	COMPLETE	PROJECT BUDGET
MULTI-PROJECT OVERHEAD	ONGOING	ONGOING	\$25,000
RE-ROOFING	COMPLETE	COMPLETE	\$925,529
WPENS RELOCATION & SITE WORK	CANCELLED	CANCELLED	\$41,858
NEW KINDERGARTEN BUILDING & SITE WORK	FUTURE BOND	FUTURE BOND	\$92,477
NEW CLASSROOM BUILDING & SITE WORK	COMPLETE	COMPLETE	\$4,150,000
CLASSROOM MODERNIZATION (PHASE 1)	04/01/2020	11/06/2020	\$6,000,442
CLASSROOM MODERNIZATION (PHASE 2)	04/01/2020	12/31/2020	\$225,518
PORTABLE DEMOLITION & SITE WORK	06/15/2021	08/23/2021	\$83,213
SITE INFRASTRUCTURE			\$10,984
CARD ACCESS SECURITY SYSTEM	06/10/2019	08/21/2021	\$190,000
DATA INFRASTRUCTURE IMPROVEMENTS	06/10/2019	08/21/2021	\$453,169
		TOTAL	\$12,198,190

OVERALL SITE BUDGET: \$12,384,192 ESTIMATED REMAINING BUDGET: \$186,000





#### CLASSROOM MODERNIZATION (UPDATED TIMELINES)

- ✤ CLASSROOM CONSTRUCTION MARCH 2020 DECEMBER 2020
- ✤ ADMINISTRATION CONSTRUCTION MAY 2020 OCTOBER 2020
- ✤ CLASSROOM MOVES END OF CALENDAR YEAR 2020


### UNFUNDED PROJECTS (FUTURE BOND)

- ✤ ADDITIONAL PORTABLE DEMOLITION
- PLAYGROUND EXPANSION
- ✤ FUTURE KINDERGARTEN CLASSROOMS
- ✤ SPECIAL NEEDS CLASSROOMS
- ✤ MULTIPURPOSE ROOM UPDATE

PROJECT PRIORITIES



QUESTIONS

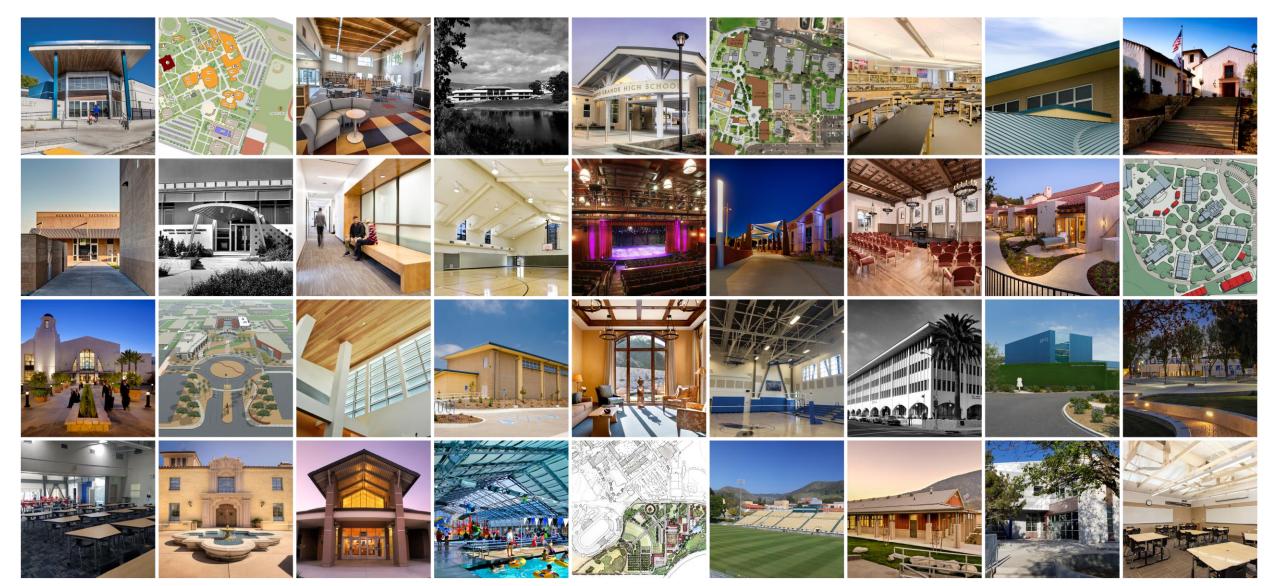



Thank You

