

Measure B **Bay View Elementary Campus Updates**





JUNE 01, 2020

AGENDA



MASTER PLAN



PROJECT BUDGETS



CLASSROOM MODERNIZATION



PORTABLE DEMOLITION




PLANNING & FUTURE PROJECTS





2020 CAMPUS MASTER PLAN

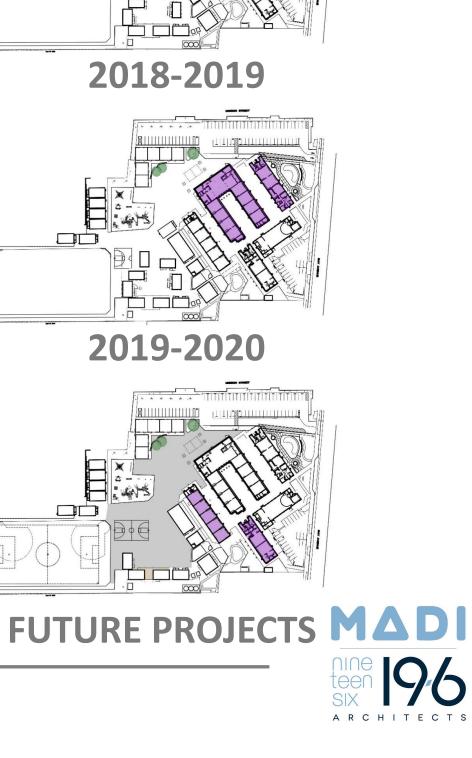



Bay View Elementary School – Measure B

PROJECT	START	COMPLETE	PROJECT BUDGET
Multi-Project Overhead	ONGOING	ONGOING	\$25,0000
Re-Roofing	COMPLETE	COMPLETE	\$925,529
WPENS Relocation & Site Work	CANCELLED	CANCELLED	\$41,858
New Kindergarten Building & Site Work	FUTURE BOND	FUTURE BOND	\$92,477
New Classroom Building & Site Work	COMPLETE	COMPLETE	\$4,569,873
Classroom Modernization (PHASE 1)	04/01/2020	08/07/2020	\$6,005,920
Classroom Modernization (PHASE 2)	04/01/2020	08/07/2020	\$225,518
Portable Demolition & Site Work	06/15/2021	08/23/2021	\$0
Site Infrastructure			\$7,484
Card Access Security System	06/10/2019	08/21/2021	\$190,000
Data Infrastructure Improvements	06/10/2019	08/21/2021	\$300,000
		TOTAL	\$12,383,659
PROJECT BUDGETS - UPDATED			ΜΔΙ



Bay View Elementary School Bond Projects

OVERALL SITE BUDGET: \$12,384,192









MODERNIZATION – CLASSROOM MODERNIZATION RENDER



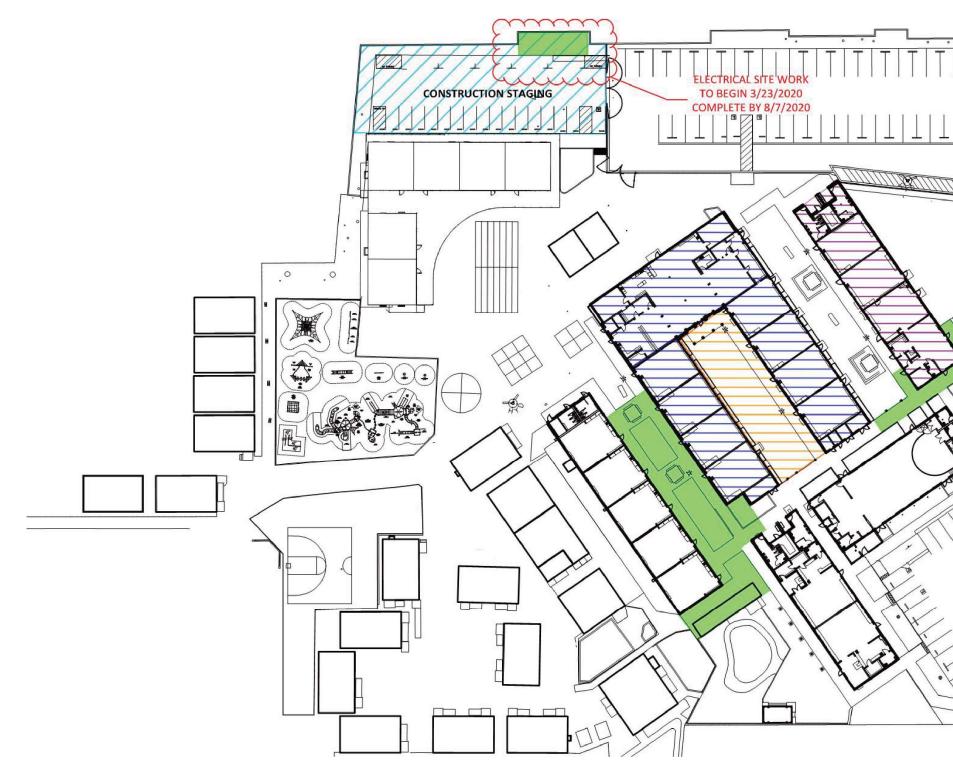



CLASSROOM MODERNIZATION – CONSTRUCTION PHASING










CAMPUS MODERNIZATION - ADMINISTRATION




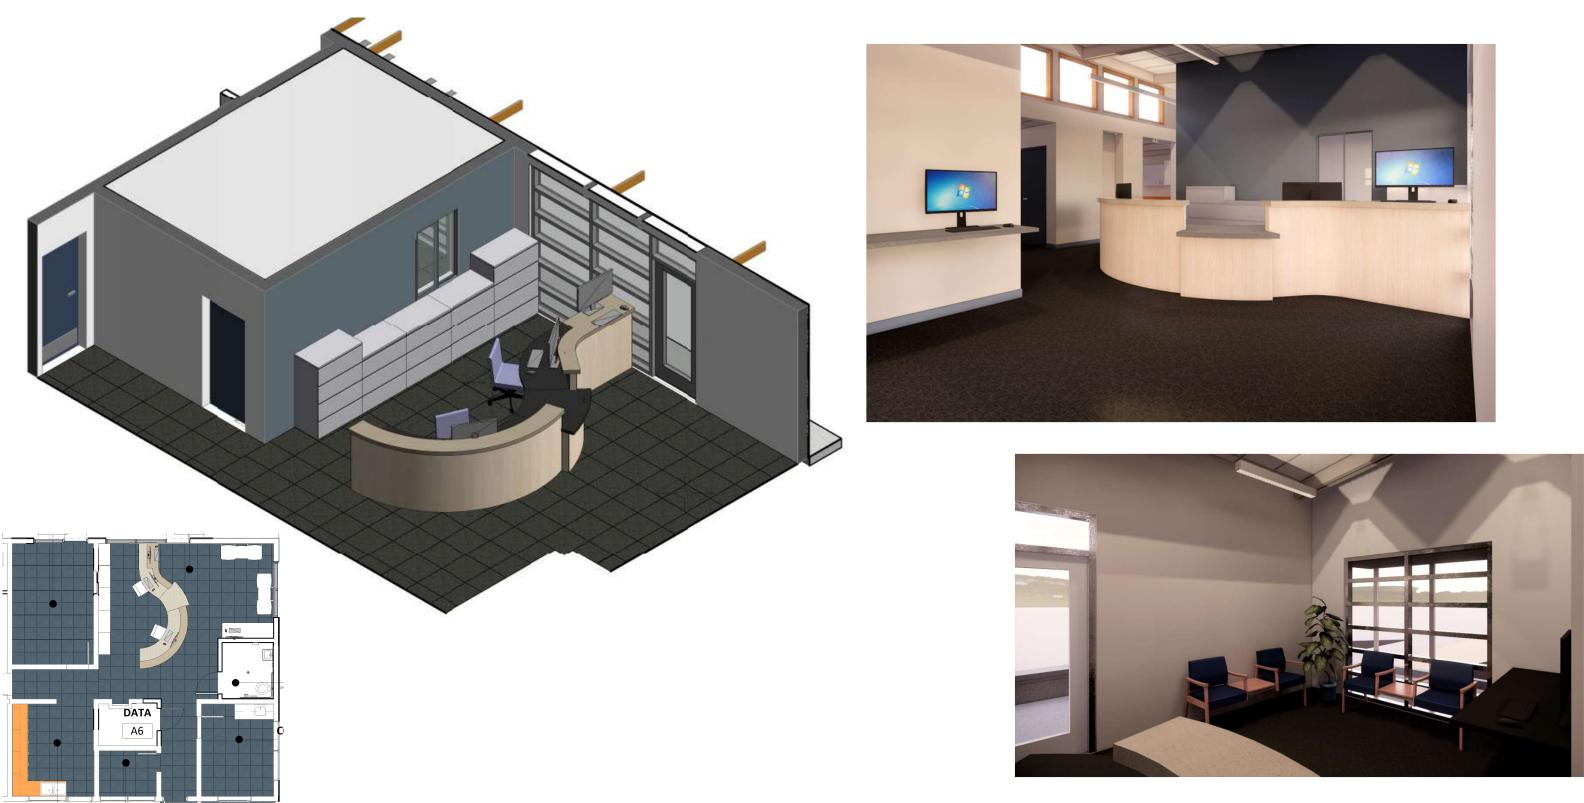



MODERNIZATION – ADMINISTRATION OFFICE



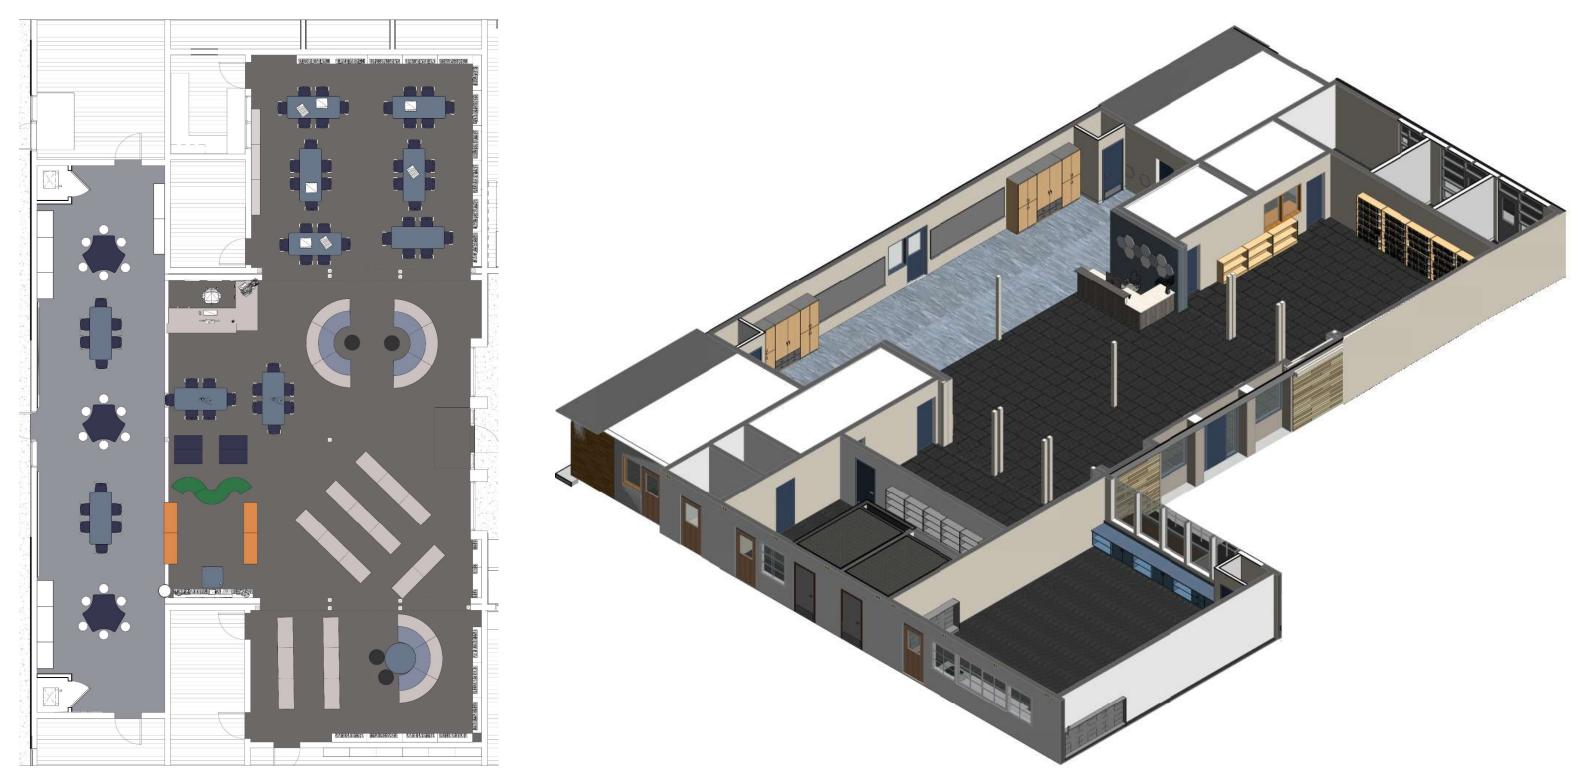












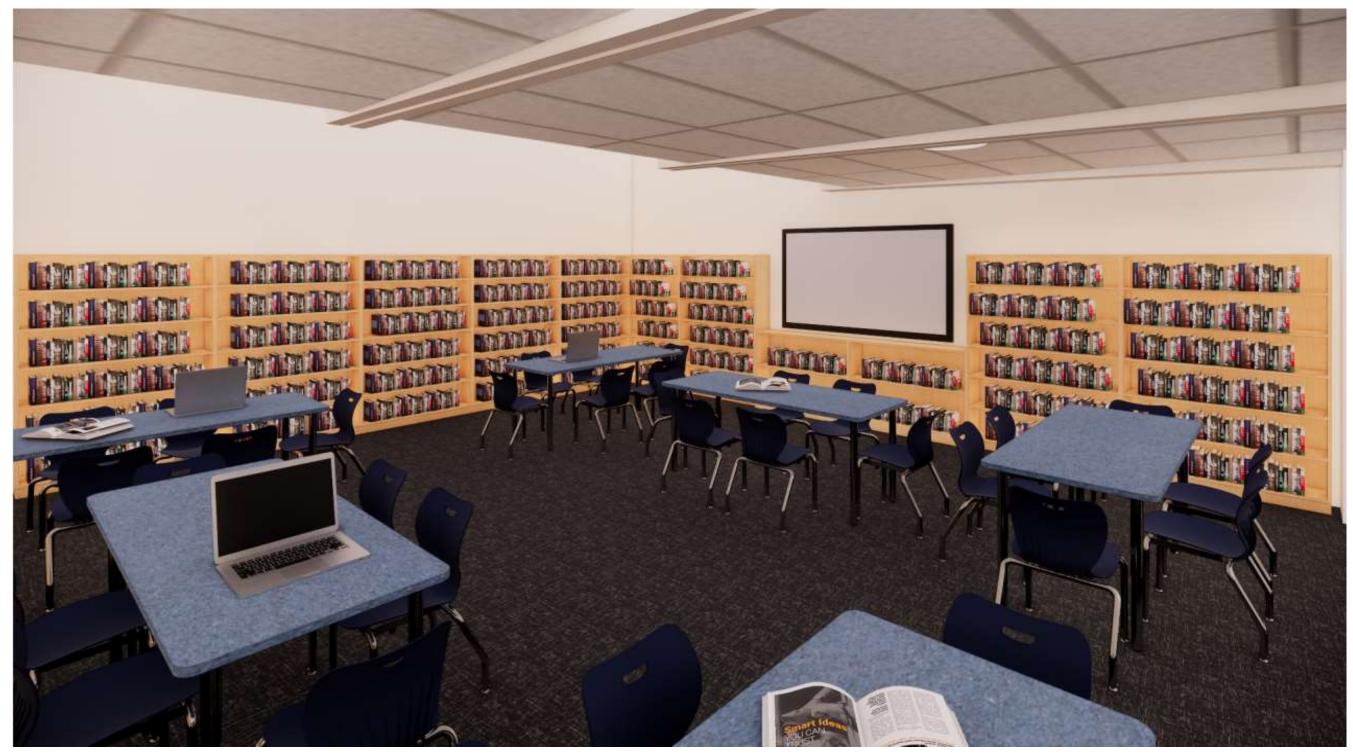












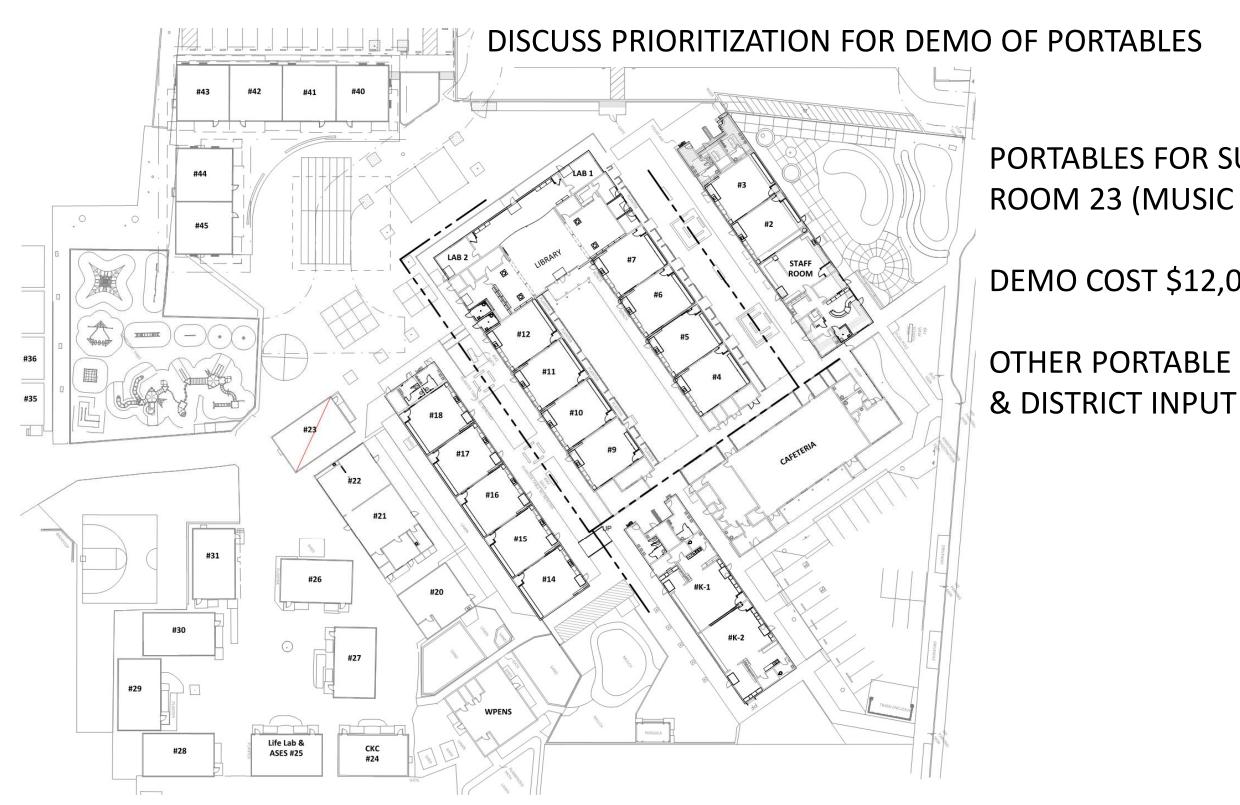



CAMPUS MODERNIZATION – PORTABLE REMOVAL PRIORITY

Bay View Elementary School Bond Projects

PORTABLES FOR SUMMER 2020 DEMO: ROOM 23 (MUSIC CLASSROOM) & ROOM 31

DEMO COST \$12,000 PER PORTABLE

OTHER PORTABLE DEMO PENDING COVID-19



PLAYGROUND STRIPING TO BE DETERMINED WITH STAFF



PHASE 1



CAMPUS MODERNIZATION – FUTURE PLAYGROUND

Bay View Elementary School Bond Projects

LEGEND

- 01 BASKETBALL COURT
- 02 TETHERBALL COURTS
- <u>0</u>3 BALL WALL
- 04 HANDBALL
- 05 FOURSQUARE COURTS

00 COLOR CIRCLE

- 0 NINE SQUARE COURT
- 08 RUNNING & RELAYS
- 09 SHADE STRUCTURE
- 🔟 TREE
- 1 PORTABLE
- 12 USA MAP (OPTIONAL)
- 13 PLAYGROUND

ASPHALT BLACKTOP



SCHEDULE:

A CLASSROOM MODERNIZATION

- CLASSROOM CONSTRUCTION MARCH 2020-JULY 2020
- > ADMIN & LIBRARY CONSTRUCTION MAY 2020-AUGUST 2020
- ➤ CLASSROOM MOVES WEEK OF JULY 27TH, 2020

A FUTURE PROJECTS

- > PORTABLE DEMOLITION (PENDING COVID 19)
- PLAYGROUND EXPANSION

A UNFUNDED PROJECTS (FUTURE BOND)

- FUTURE KINDERGARTEN CLASSROOMS
- SPECIAL NEEDS CLASSROOMS



WHAT'S NEXT



THANK YOU!
