

Gault Elementary School | Update

SANTA CRUZ CITY SCHOOLS | BOND COMMITTEE- 29 JANUARY 2020

BARTOS
ARCHITECTURE

COLLABORATION
ADVOCACY
RESEARCH
EDUCATION

Past

- ✓ Historic Roof Restoration: Complete.
- ✓ Water Intrusion at “Swamp” Repairs, Complete.
- ✓ Exterior Building Paint, Complete.

Ongoing


- Site Security
- Classroom Technology

Future

- Classroom Furniture
- Relocation / site preparation for New Building
- New Two-Story Modular Classroom Building

Bond Committee Update: Gault Elementary School

- Anticipated Construction schedule**
- WINTER 2017
 - SUMMER 2018
- Projects**
- Miscellaneous Projects**
- Remove Portables**
 - Water intrusion repair
 - Tile Roof Replacement
 - New Classroom Building
 - Lunch Canopy
 - Play yard Reconfiguration
 - Exterior Painting
- Master Plan Project Categories**
- Building Modernization
 - HVAC System Improvement
 - Utility Infrastructure
 - Exterior Painting
 - Re-Roofing
 - Landscape and Irrigation
 - Portable Replacement/ New Construction
 - Kitchen Relocation
 - Shade Canopy Additions
 - Student Drop off and Parking Areas

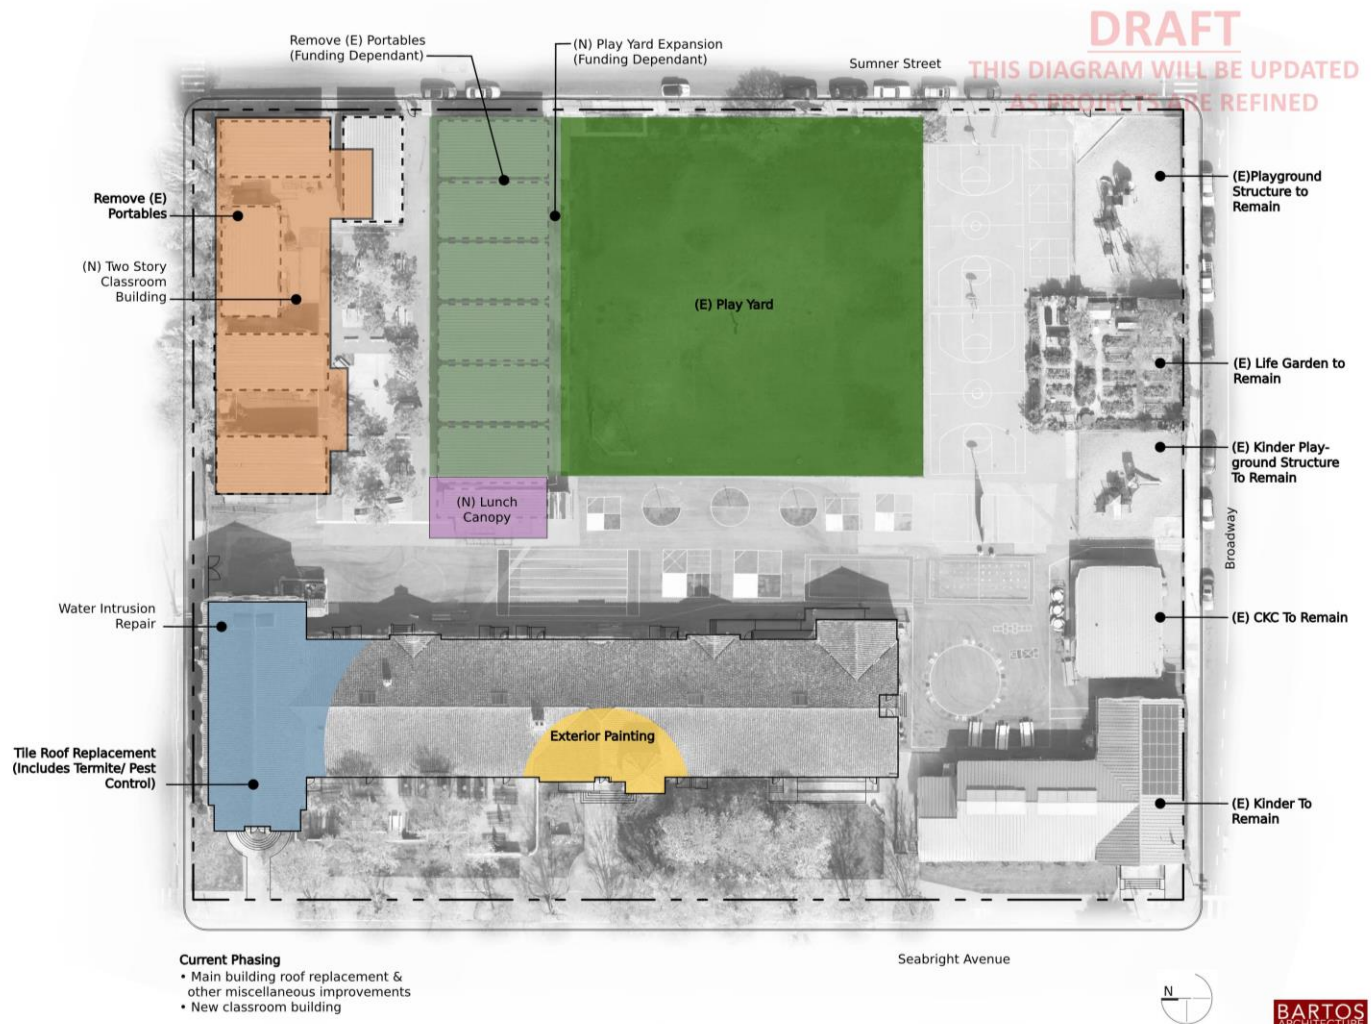

Gault Elementary School
Santa Cruz City Schools





Revised Master Plan to be reviewed by Bond Site Committee on 29 January 2020

Bond Committee Update: Gault Elementary School



Proposed New Modular Building


Bond Committee Update: Gault Elementary School

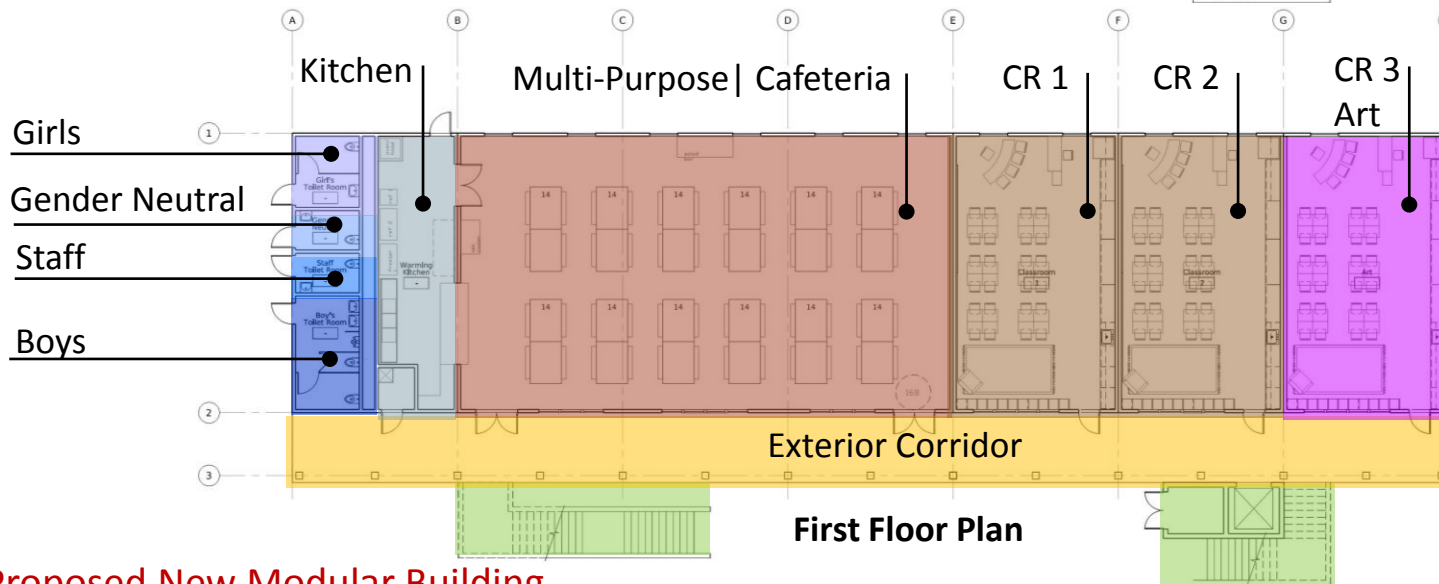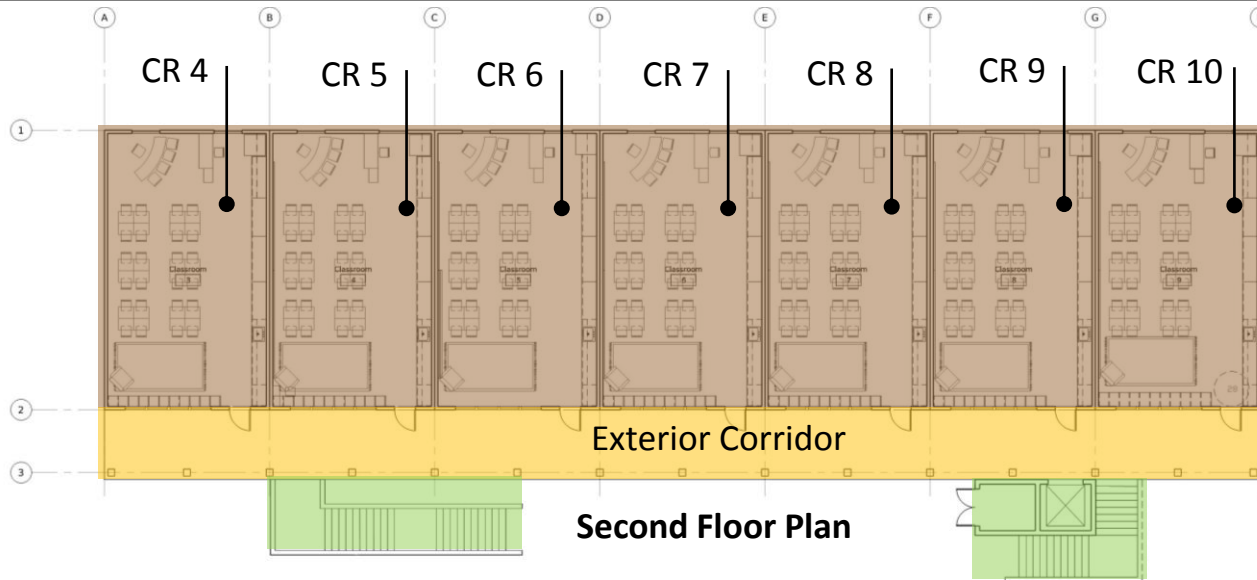



Proposed New Modular Building

Bond Committee Update: Gault Elementary School

Readers Workshop

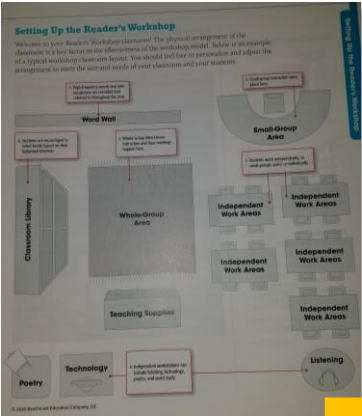

Collaboration

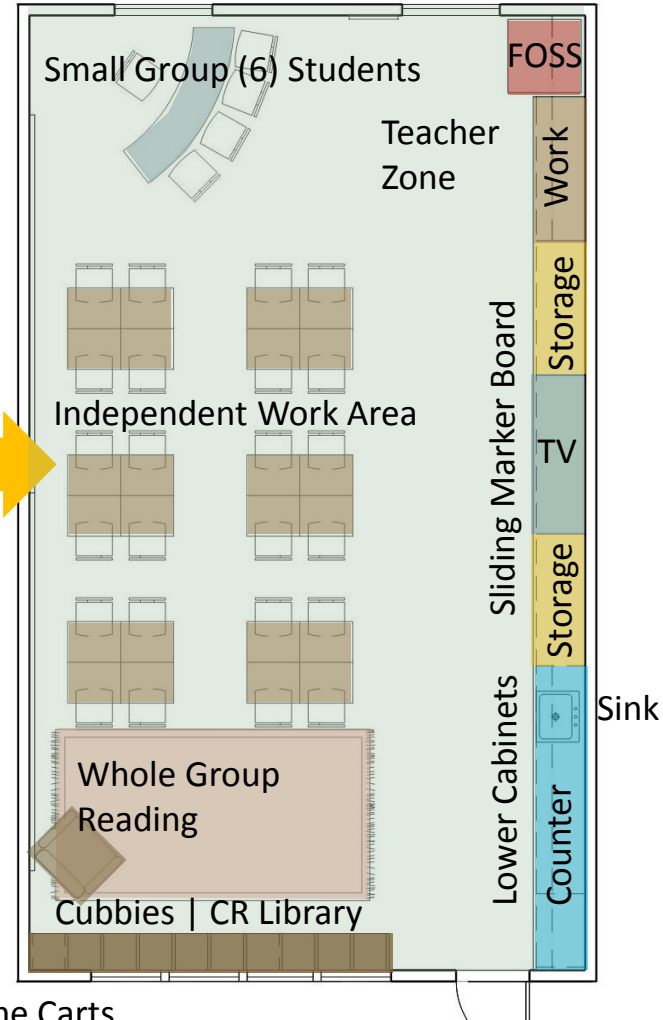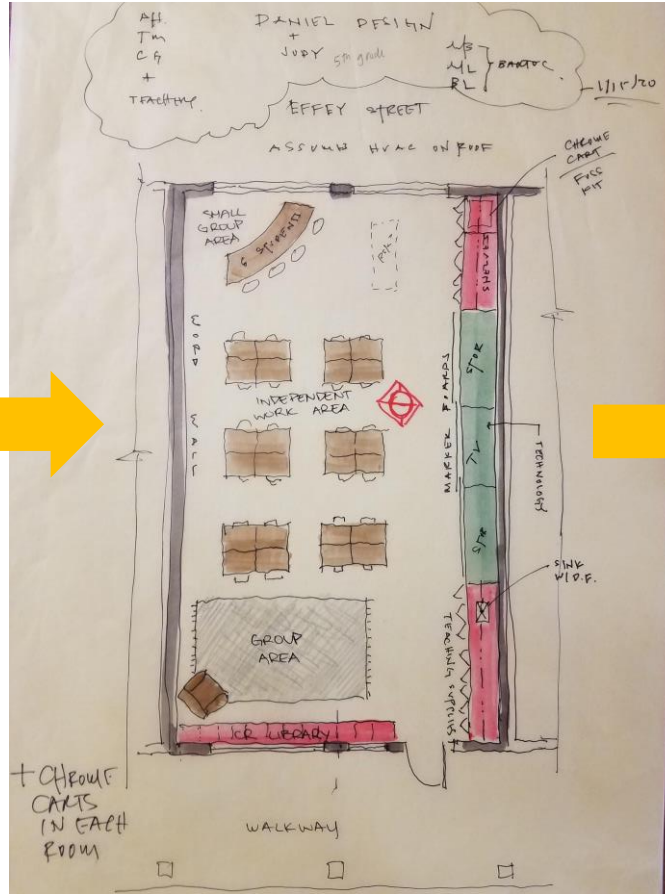

Chrome Carts

Work area arrangement varies with grade/teacher

Proposed New Modular Building Classroom

Bond Committee Update: Gault Elementary School

Project	Allocation	Status
Multi Project Overhead	\$560,871	Ongoing
Roofing	\$798,937	Complete
Main Building Paint	\$248,270	Complete
Card Access Security System	\$100,000	Ongoing
Data Infrastructure	\$231,708	Ongoing
New Classroom Building	\$6,091,542	Fall 2022 (occupy)
Remove portables, Field	\$982,682	Summer 2022
New Lunch Shelter	\$125,000	Summer 2022
Modernization Phase 1	\$87,841	(water intrusion)
Furniture	TBD	Estimate/Layout in progress
<hr/>		
<i>Budget allocation-ROM only.</i>	\$9,226,851	
<i>Measure B Resource</i>	\$9,226,851	

Bond Committee Update: Gault Elementary School

END

Project	Allocation	Status
Multi Project Overhead	\$560,871	Ongoing
Roofing	\$798,937	Complete
Main Building Paint	\$248,270	Complete
Card Access Security System	\$100,000	Ongoing
Data Infrastructure	\$231,708	Ongoing
New Classroom Building	\$6,091,542	Fall 2022 (occupy)
Remove portables, Field	\$982,682	Summer 2022
New Lunch Shelter	\$125,000	Summer 2022
Modernization Phase 1	\$87,841	(water intrusion)
Furniture	TBD	Estimate/Layout in progress
<hr/>		
<i>Budget allocation-ROM only.</i>	\$9,226,851	
<i>Measure B Resource</i>	\$9,226,851	

PLEASE NOTE: OUR ESTIMATE FOR THE NEW BUILDING AS CURRENTLY PROGRAMED IS \$8.2-8.5M.
