



Measure B
MADI 19six Architects Project Updates



OCTOBER 29, 2020



AGENDA

PROJECT BUDGETS

REVIEW PREVIOUS PROJECTS

ONGOING MODERNIZATION

SITE PROJECT PRIORITY LIST

DELAVEAGA ELEMENTARY SCHOOL – MEASURE B



PROJECT	START	COMPLETE	PROJECT BUDGET
Multi-Project Overhead	ONGOING	ONGOING	\$30,000
NEW SHADE STRUCTURE & Parking lot	COMPLETE	COMPLETE	\$1,372,745
New Classroom Building & site work	complete	complete	\$4,789,309
Modernization (PHASE 1)	08/01/2018	12/30/2020	\$7,357,133
Modernization (PHASE 2)	08/01/2018	12/30/2020	\$339,500
Portable Demolition & Site Work	06/15/2021	08/23/2021	\$100,000
Site infrastructure	ongoing	ongoing	\$6,098
Card Access Security System	06/10/2019	08/21/2021	\$164,560
Data Infrastructure Improvements	06/10/2019	08/21/2021	\$334,542
		Site budget	\$14,188,861

DELAVEAGA ELEMENTARY SCHOOL – NEW CLASSROOM BUILDING



DELAVEAGA ELEMENTARY SCHOOL – NEW CLASSROOM BUILDING



DELAVEAGA ELEMENTARY SCHOOL – ADMINISTRATION ENTRANCE




MADI
nineteen
six
ARCHITECTS



NEW FRONT ENTRANCE TO THE CAMPUS

DELAVEAGA ELEMENTARY SCHOOL – ADMINISTRATION

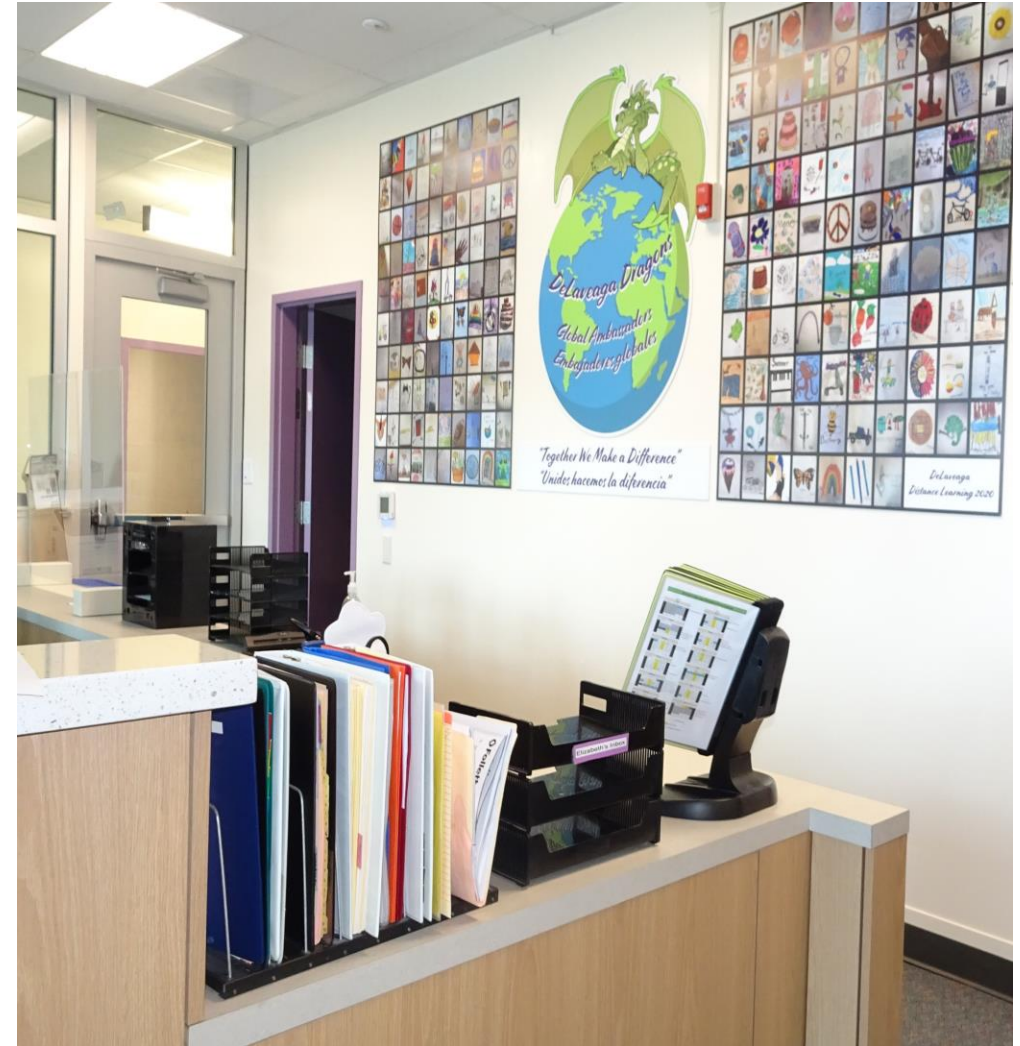

NEW ADMINISTRATION ENTRANCE



NEW WAITING AREA (RENDER)

NEW WAITING AREA



PRINCIPAL'S OFFICE



PRINCIPAL'S OFFICE (RENDER)



DELAVEAGA ELEMENTARY SCHOOL – STAFF LOUNGE




STAFF LOUNGE (RENDER)




STAFF LOUNGE (90% COMPLETE)



DELAVEAGA ELEMENTARY SCHOOL – STAFF LOUNGE

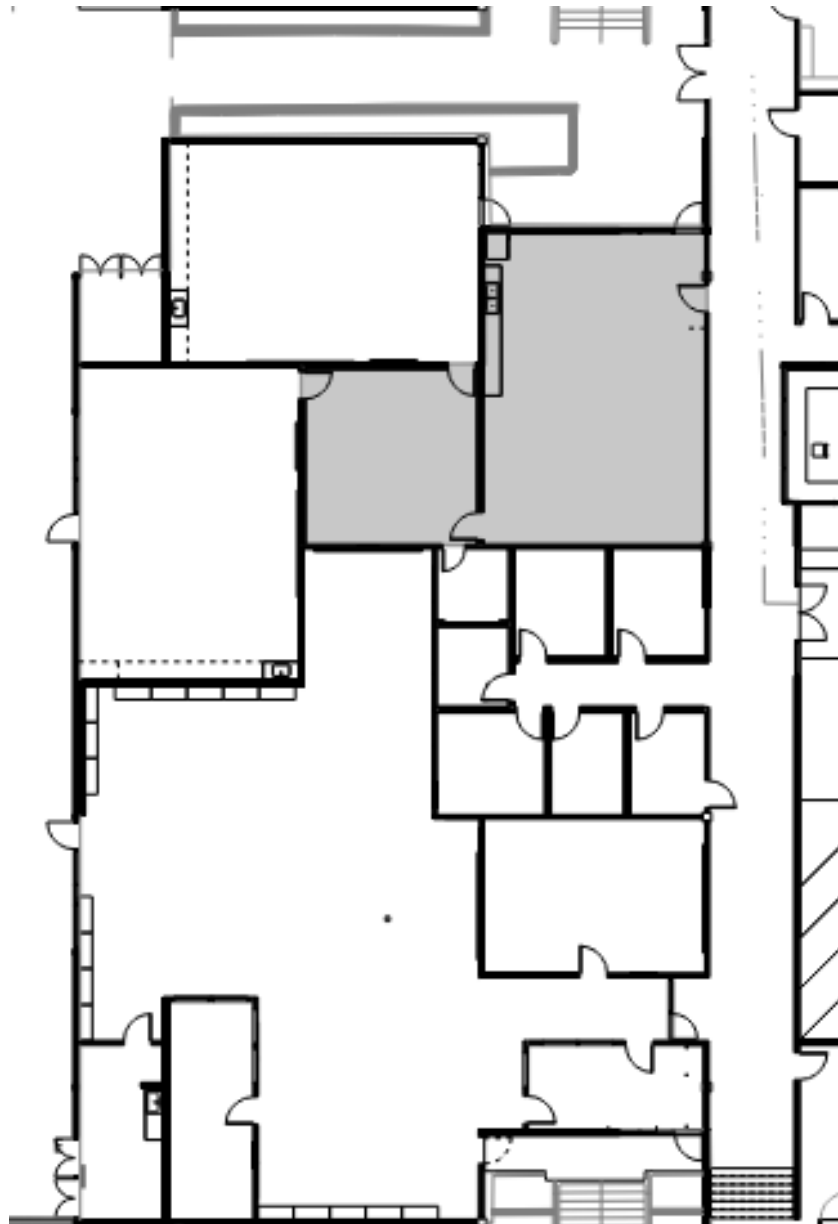

DELAVEAGA ELEMENTARY SCHOOL – NEW OFFICES

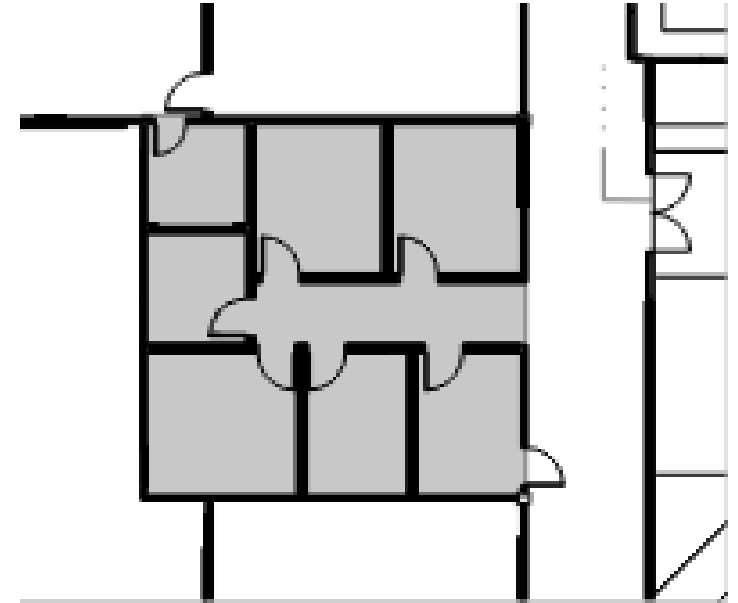

DELAVEAGA ELEMENTARY SCHOOL – LITTLE THEATRE



DELAVEAGA ELEMENTARY SCHOOL – LIBRARY & MEDIA CENTER



DELAVEAGA ELEMENTARY SCHOOL – LIBRARY & MEDIA CENTER



CAMPUS MODERNIZATION – CLASSROOM MODERNIZATION




FUTURE PROJECT – PORTABLE DEMOLITION




PORTABLES TO BE DEMOLISHED AFTER MODERNIZATION (GREY)

SCHEDULE: SUMMER 2021 COMBINE WITH FINAL BOND PROJECTS

ESTIMATED DEMO COST: \$100,000

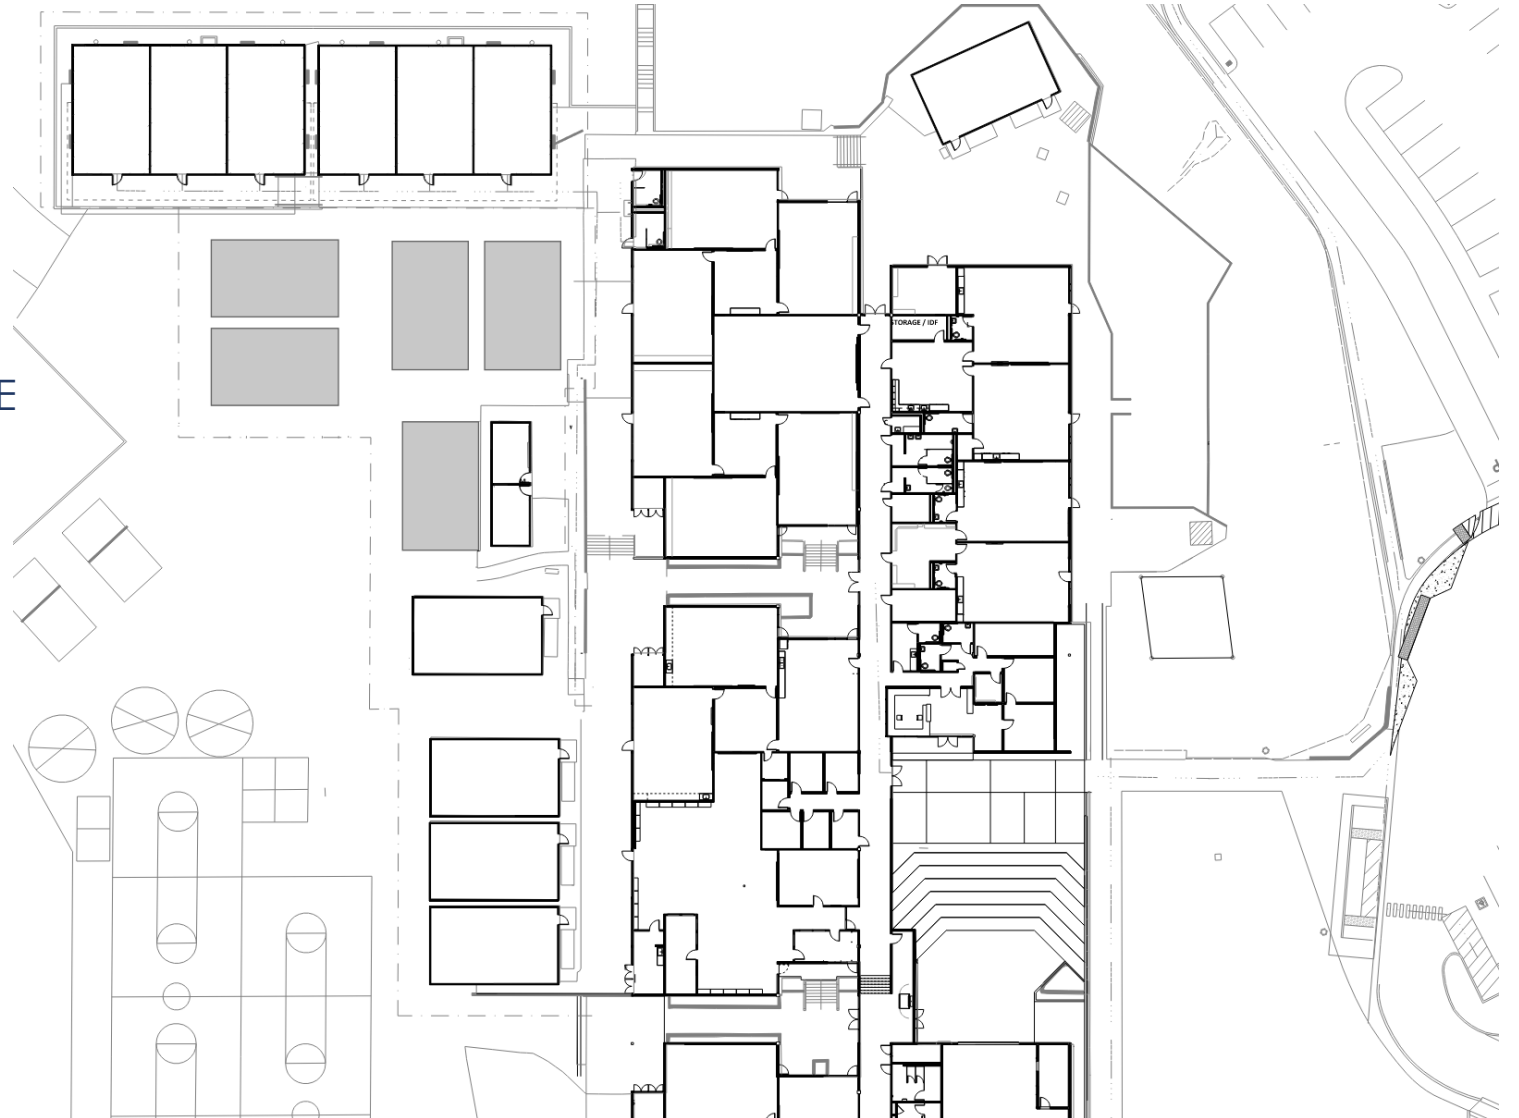

FUTURE PROJECT – RE-ROOFING

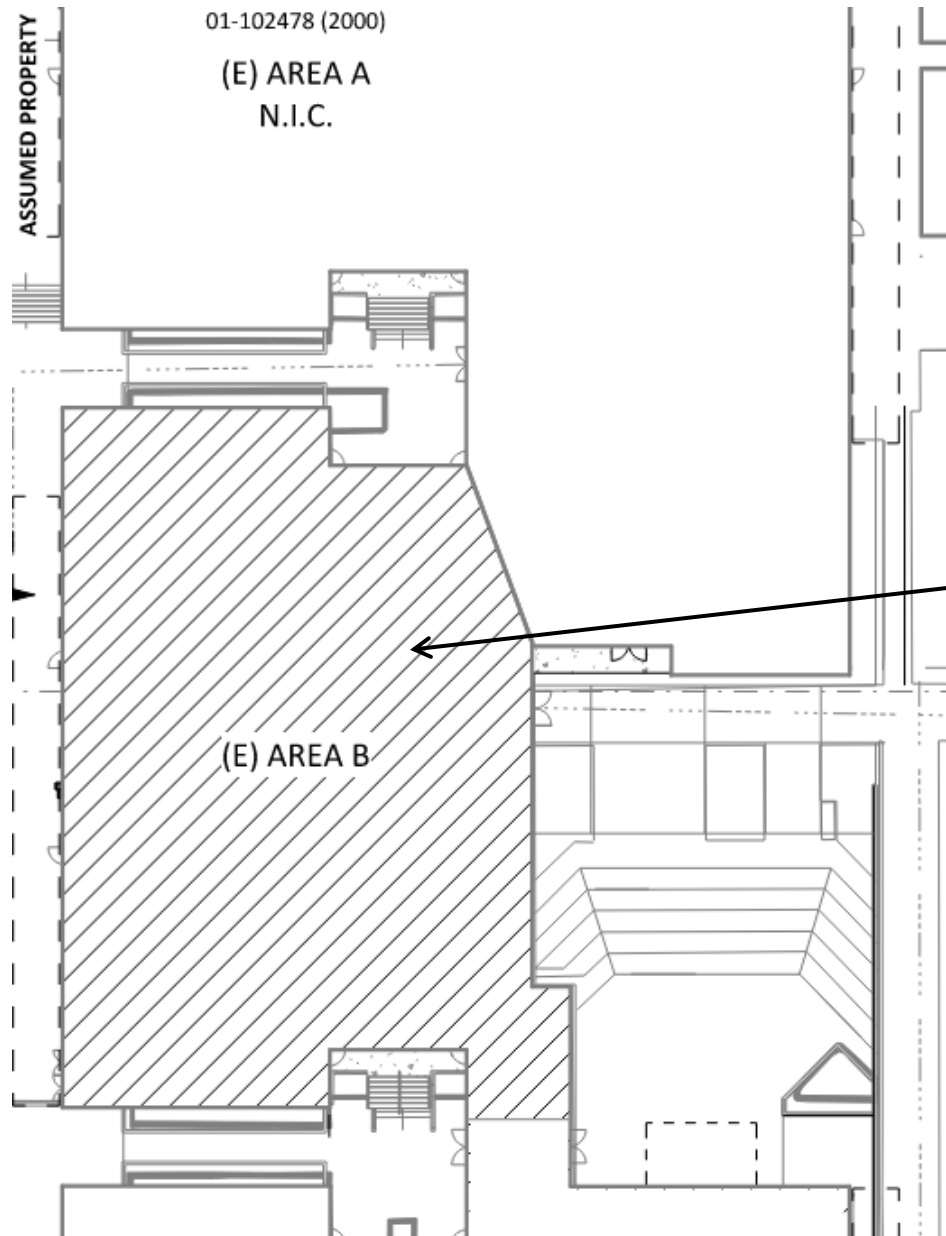

**ROOF NEEDING REPLACEMENT
(HATCHED IN GREY)**

SCHEDULE: SUMMER 2021 COMBINE
WITH FINAL BOND PROJECTS

ESTIMATED ROOF REPLACEMENT
COST: \$700,000



1. KINDERGARTEN PLAYGROUND REPAIRS
2. MAIN PLAYGROUND IMPROVEMENTS
3. MODERNIZATION OF WING C CLASSROOMS
4. MODERNIZATION OF MULTI-PURPOSE ROOM

ADDITIONAL PROJECTS NOT LISTED

DELAVEAGA ELEMENTARY SCHOOL – MEASURE B




PROJECT	START	COMPLETE	PROJECT BUDGET
Multi-Project Overhead	ONGOING	ONGOING	\$30,000
NEW SHADE STRUCTURE & Parking lot	COMPLETE	COMPLETE	\$1,372,745
New Classroom Building & site work	complete	complete	\$4,789,309
Modernization (PHASE 1)	08/01/2018	12/30/2020	\$7,357,133
Modernization (PHASE 2)	08/01/2018	12/30/2020	\$339,500
Portable Demolition & Site Work	06/15/2021	08/23/2021	\$100,000
Site infrastructure	ongoing	ongoing	\$6,098
Card Access Security System	06/10/2019	08/21/2021	\$164,560
Data Infrastructure Improvements	06/10/2019	08/21/2021	\$334,542
		Site budget	\$14,188,861

NOTE: ADDITIONAL FUNDS MAY BE AVAILABLE AFTER JANUARY 2021

QUESTIONS





Thank You

