

Gault Elementary School | Update



SANTA CRUZ CITY SCHOOLS | BOND COMMITTEE- 16 SEPTEMBER 2020

BARTOS
ARCHITECTURE

COLLABORATION
ADVOCACY
RESEARCH
EDUCATION

Bond Committee Update: Gault Elementary School

Agenda

01

Introductions

02

Review Completed Projects

03

Proposed Building Scope

04

Priorities and implementation

Schedule Next Meeting

Bond Committee Update: Gault Elementary School

Past

- ✓ Historic Roof Restoration: Complete.
- ✓ Water Intrusion at “Swamp” Repairs, Complete.
- ✓ Exterior Building Paint, Complete.


Ongoing

- Site Security-Card Access
- Classroom Technology - Data

Future

- Relocation / site preparation for New Building
- New Two-Story Modular Classroom Building


Gault Elementary School

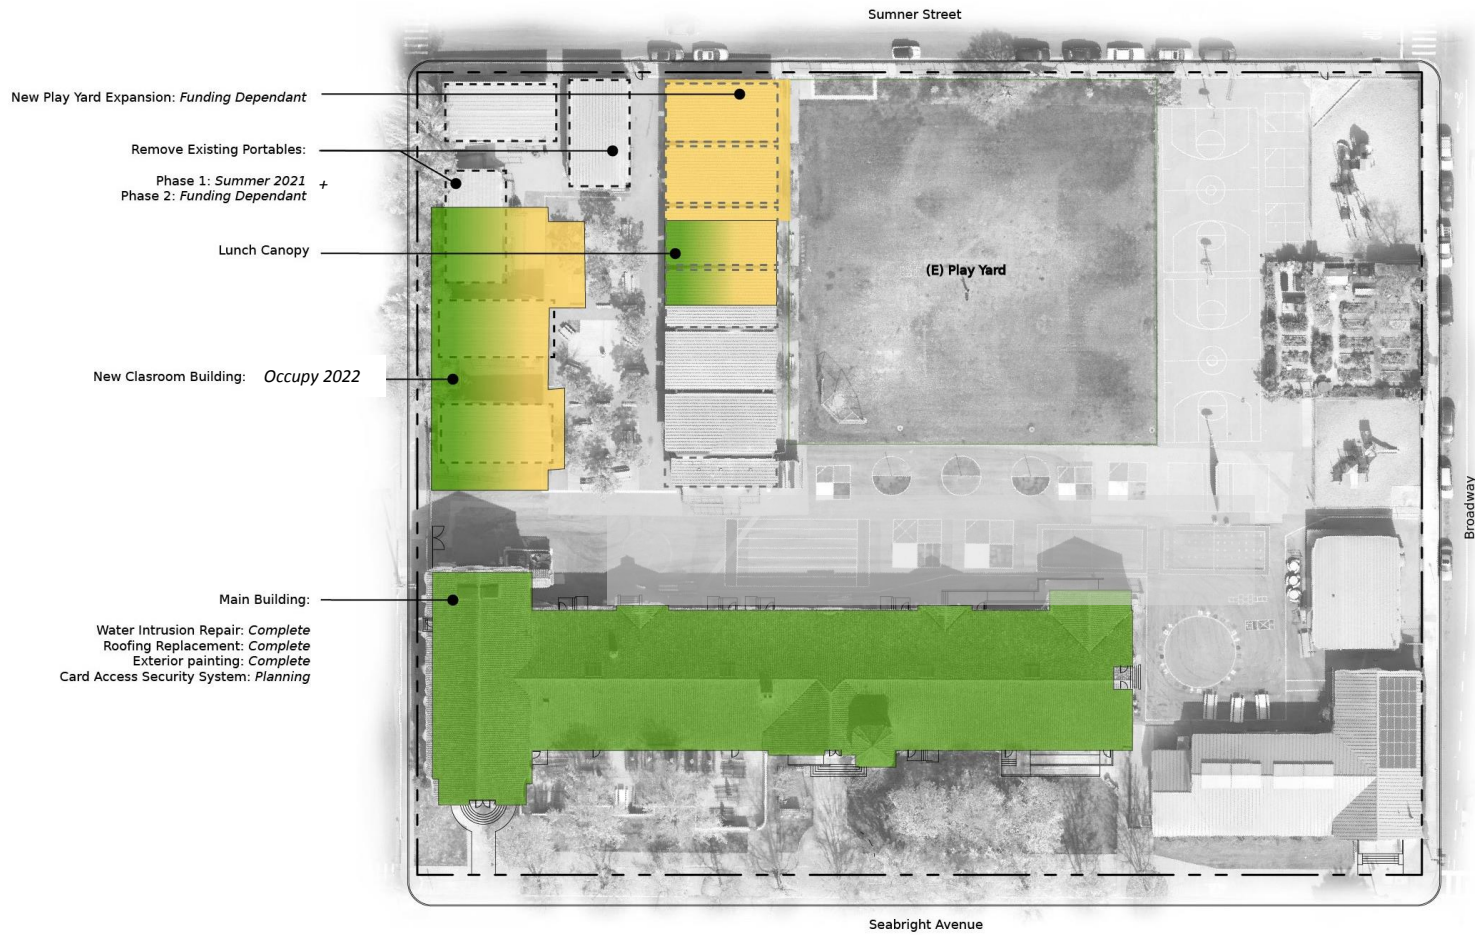

Gault Elementary School
Santa Cruz City Schools



Gault Elementary School: New Building

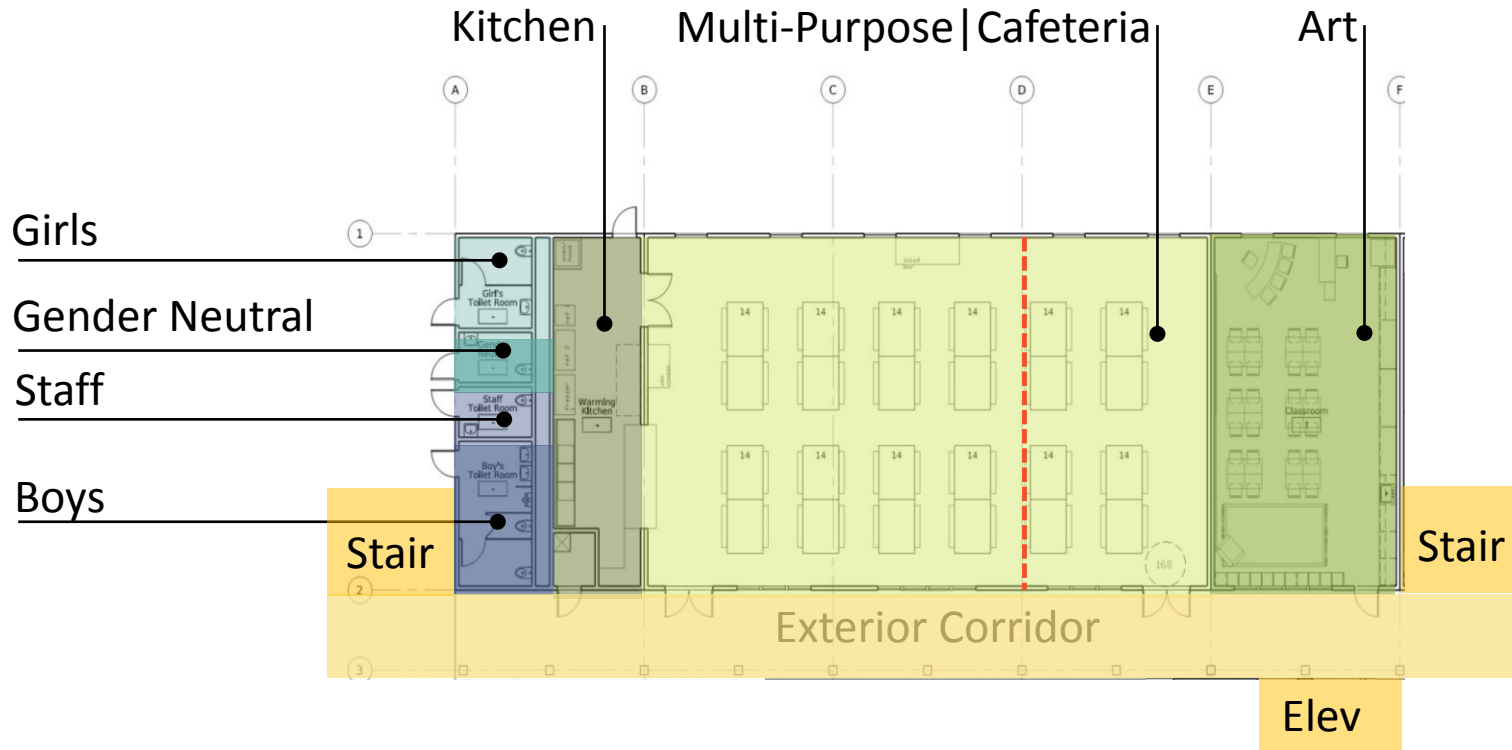


First Floor Plan

Modular Building: First Floor Scope:

- Restrooms, Kitchen, Multi-Purpose, Art

Gault Elementary School: New Building

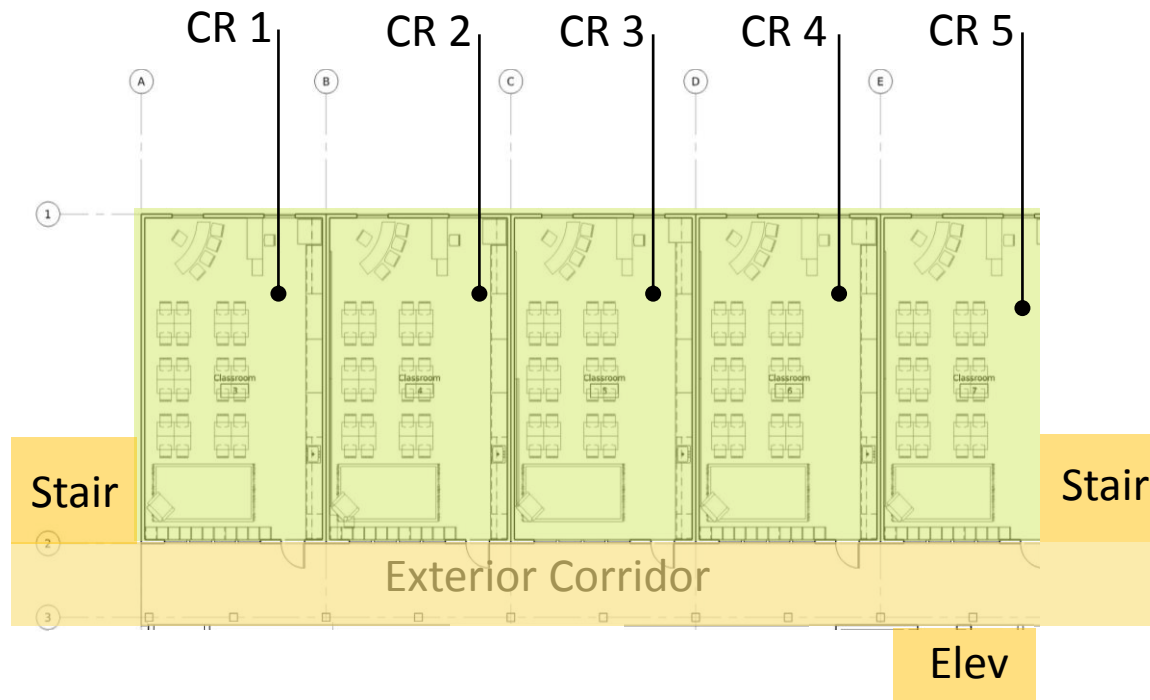


Second Floor Plan

Modular Building: Second Floor Scope:


- Five (5) classrooms

Bond Committee Update: Gault Elementary School


Readers Workshop

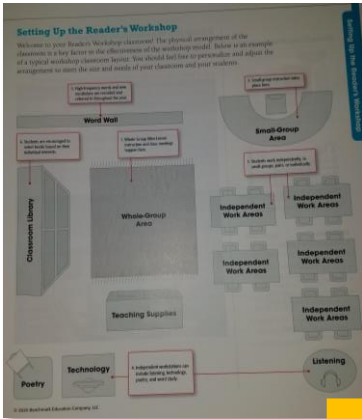

Collaboration

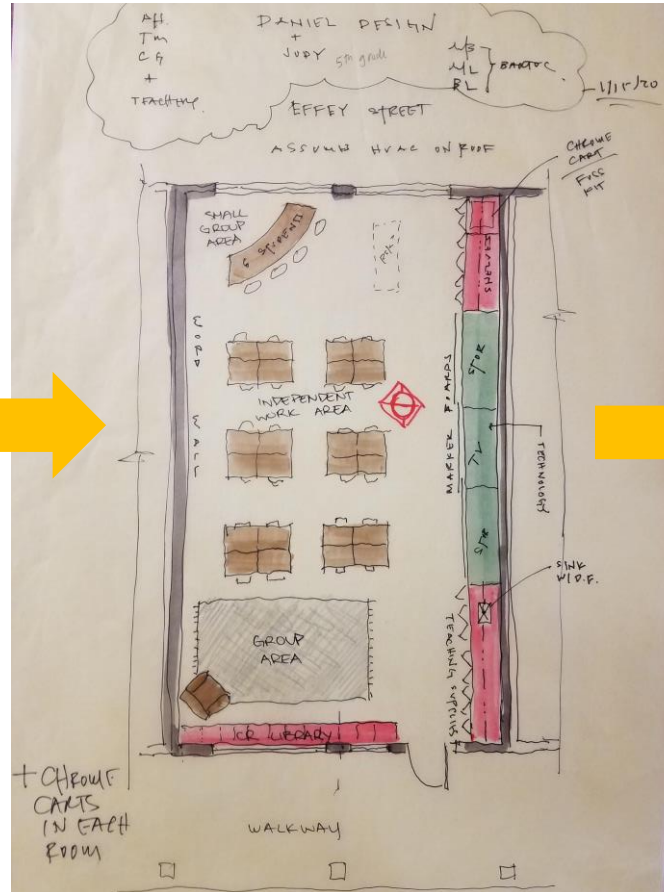

Collaboration

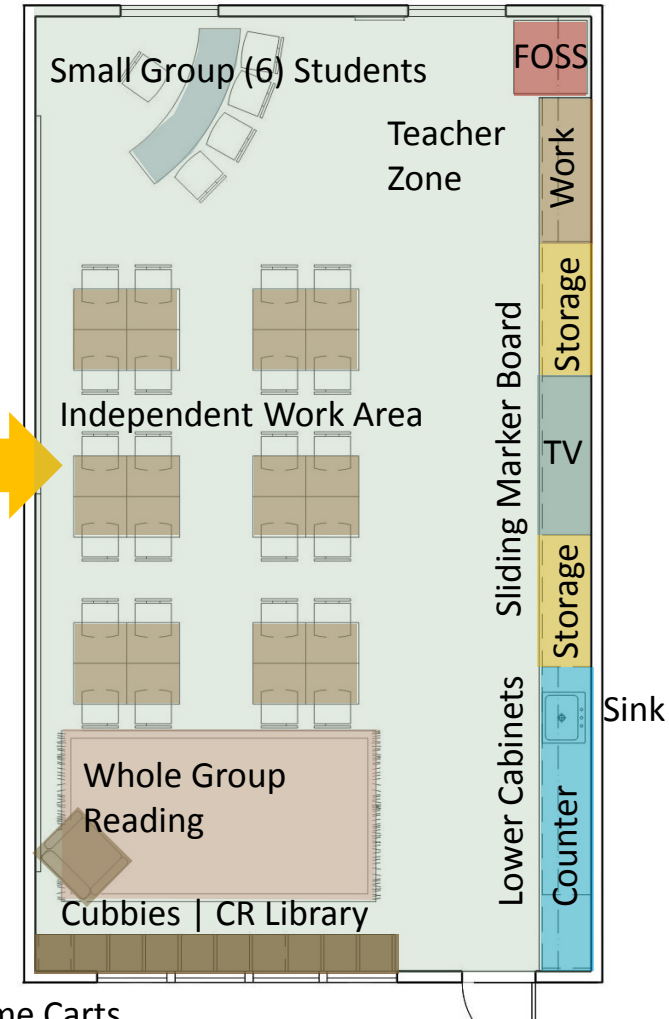


Chrome Carts

Work area arrangement varies with grade/teacher


Gault Elementary School: New Building

Kitchen will serve students in Multi Purpose room and Outside eating areas.

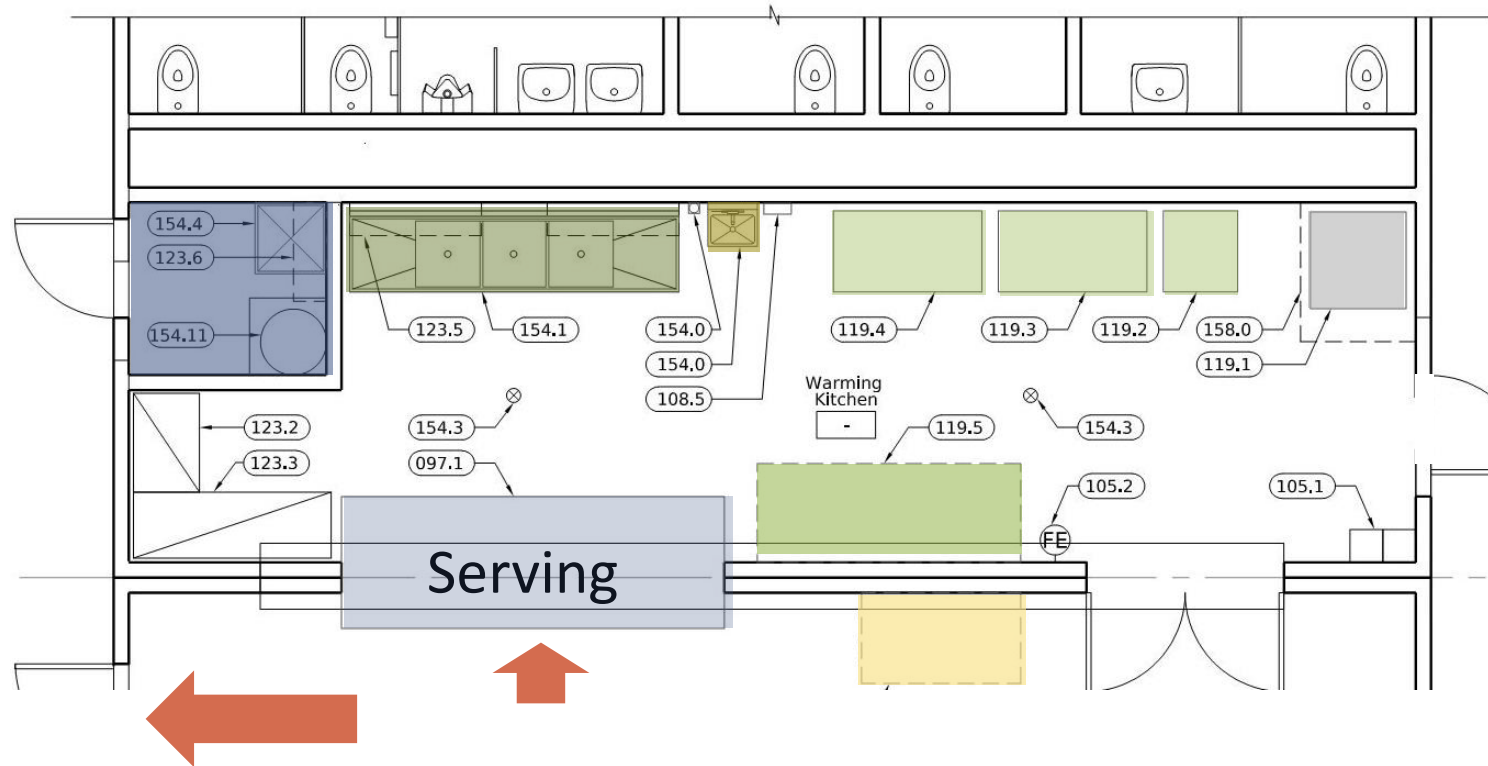


Warming Kitchen

Gault Elementary School: Masterplan

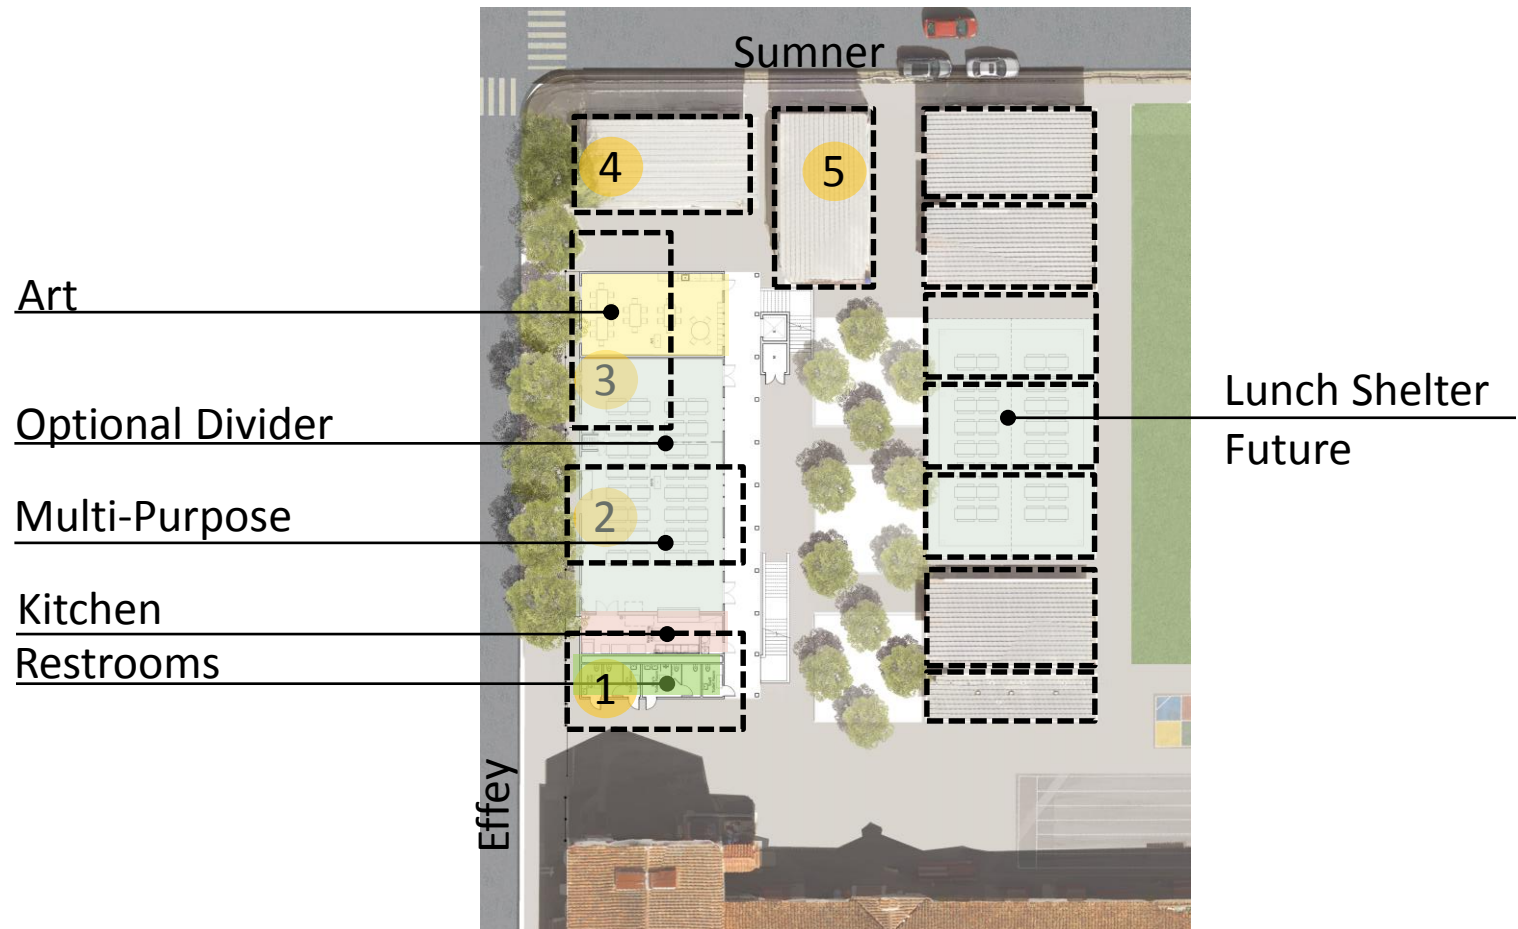

First Floor

Gault Elementary School: Masterplan

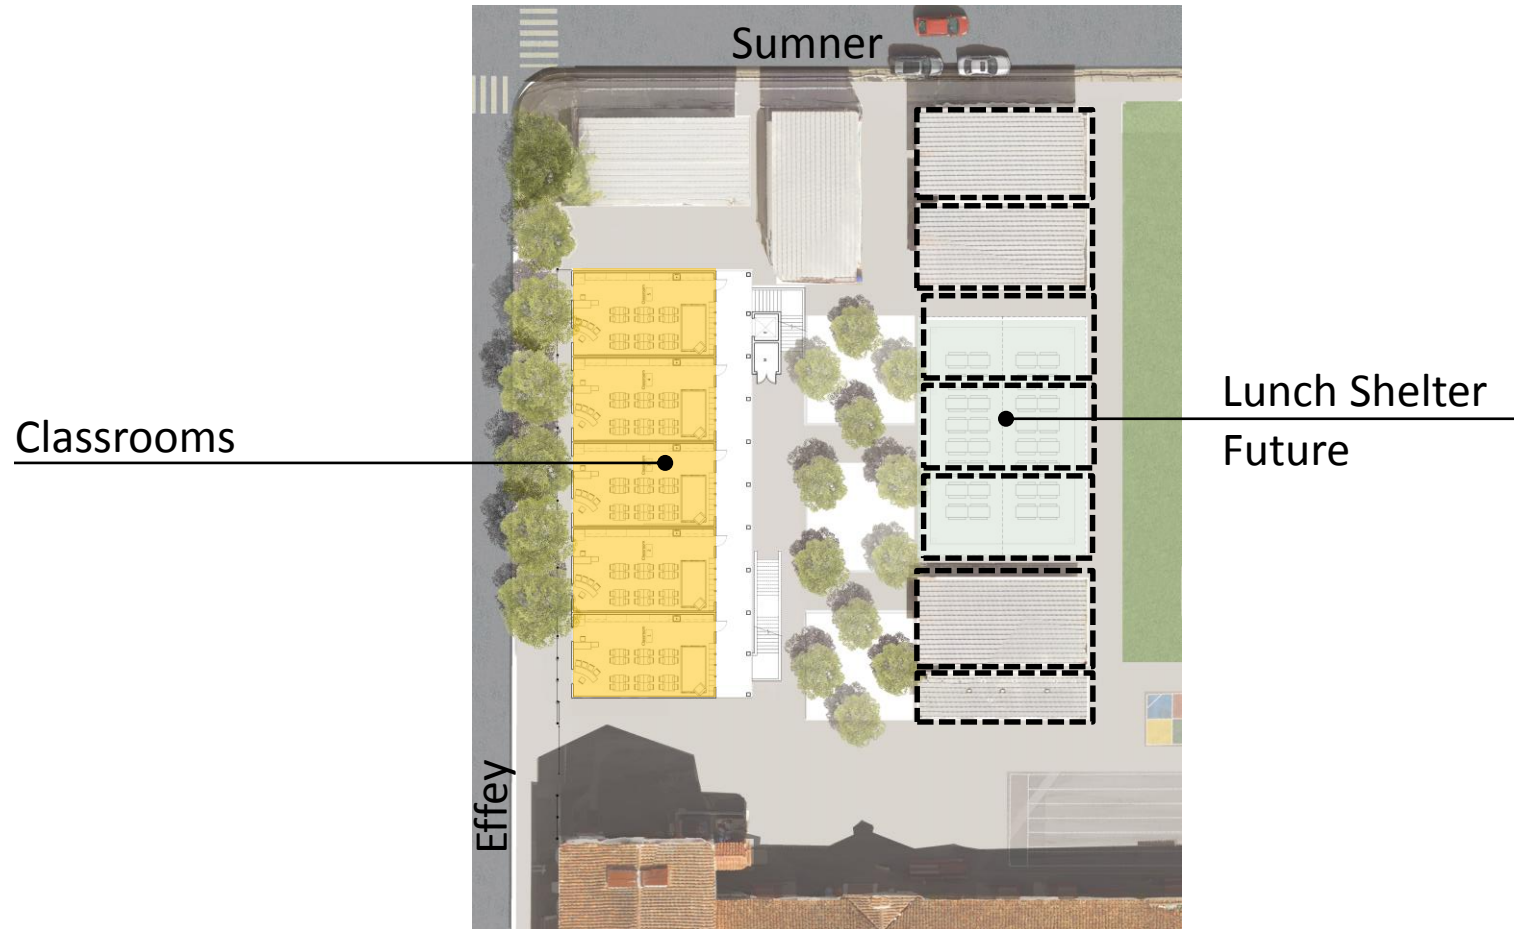

Second Floor

Bond Committee Update: Gault Elementary School

Project	Allocation	Status
Multi Project Overhead	\$560,871	Ongoing
Roofing	\$798,937	Complete
Main Building Paint	\$263,341	Complete
Card Access Security System	\$100,001	Ongoing
Data Infrastructure	\$415,607	Ongoing
New Classroom Building	\$6,250,000	2022 (occupy)
Remove portables	\$500,000	Summer 2022
New Lunch Shelter	\$125,000	Summer 2022
Modernization Phase 1	\$99,189	(water intrusion)
Utility Infrastructure	43,896	
Furniture	TBD	
<i>Budget allocation-ROM only.</i>	\$9,156,842	
<i>Measure B Resource</i>	\$9,226,851	

Bond Committee Update: Gault Elementary School

Agenda

01

Introductions

02

Review Completed Projects

03

Proposed Building Scope

04


Priorities and implementation

Schedule Next Meeting

Bond Committee Update: Gault Elementary School


END

Gault Elementary School: Masterplan

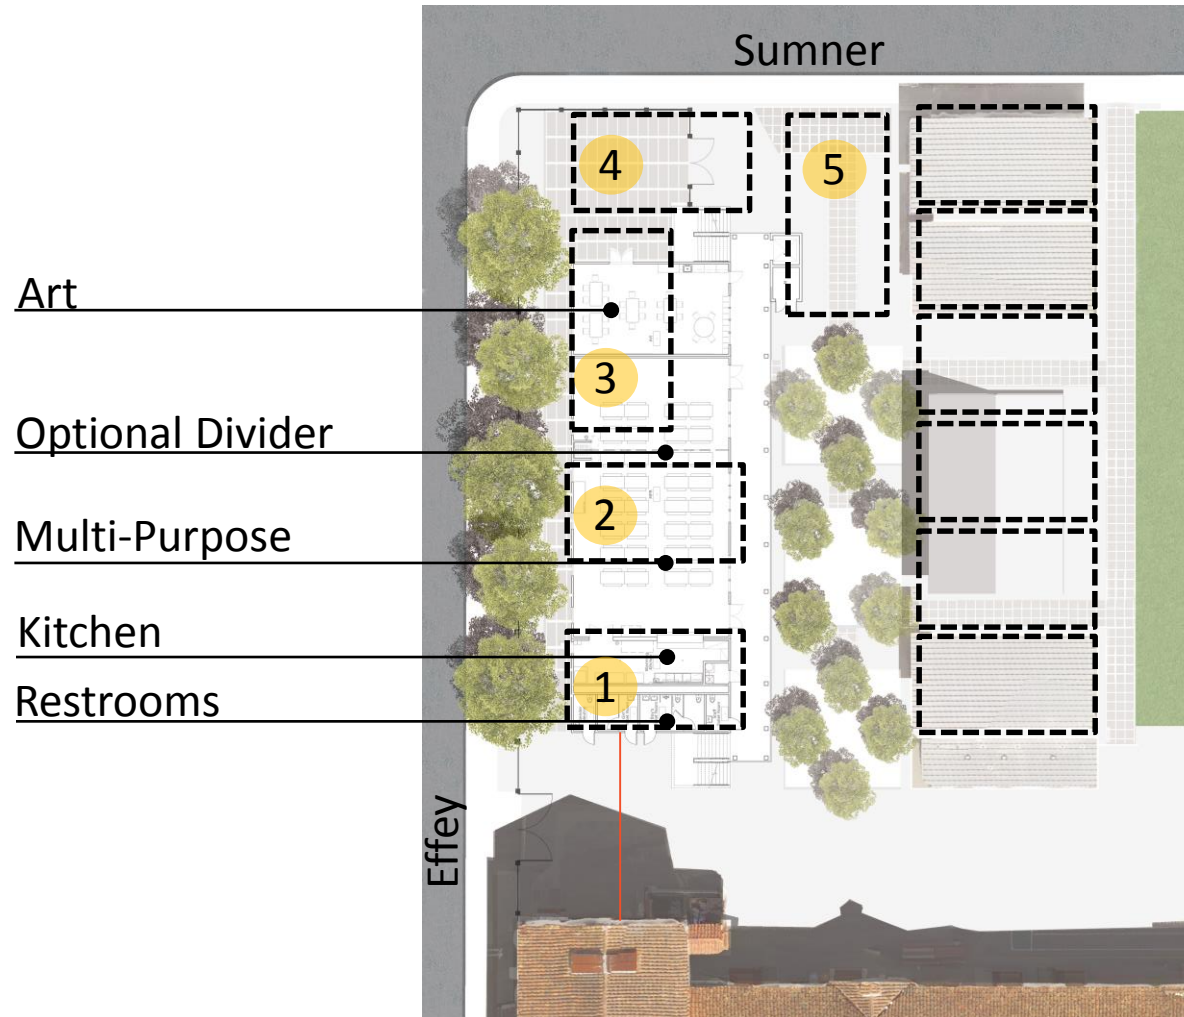


Step | Phase 1

Gault Elementary School: Masterplan

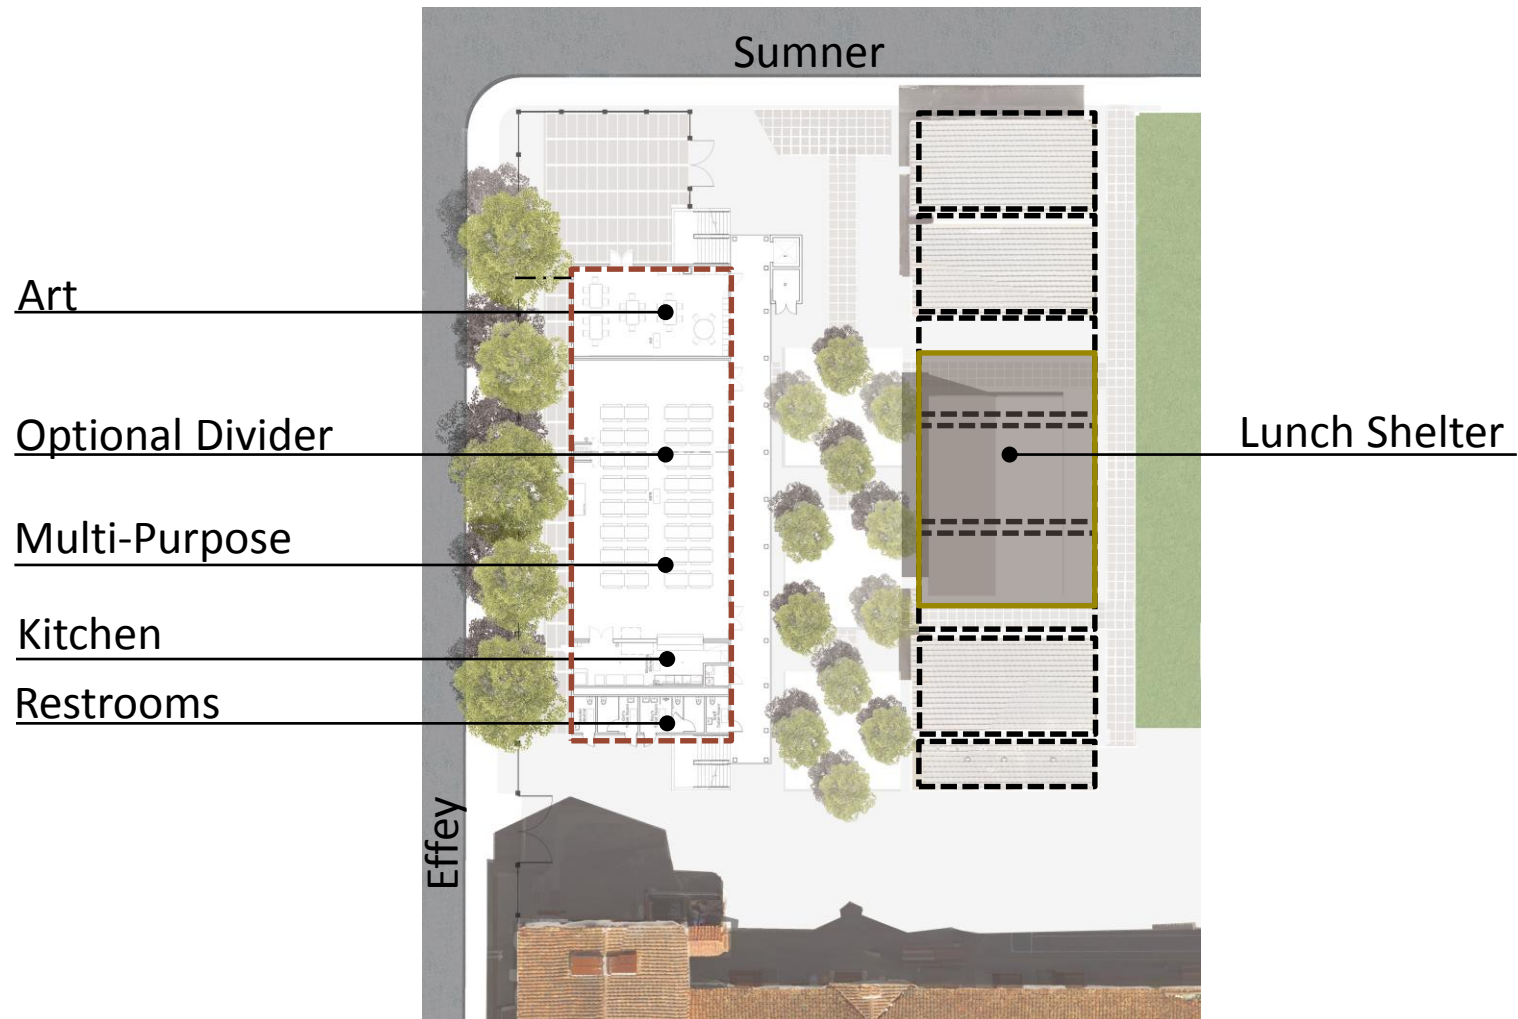


Step | Phase 2: Building

Gault Elementary School: Masterplan

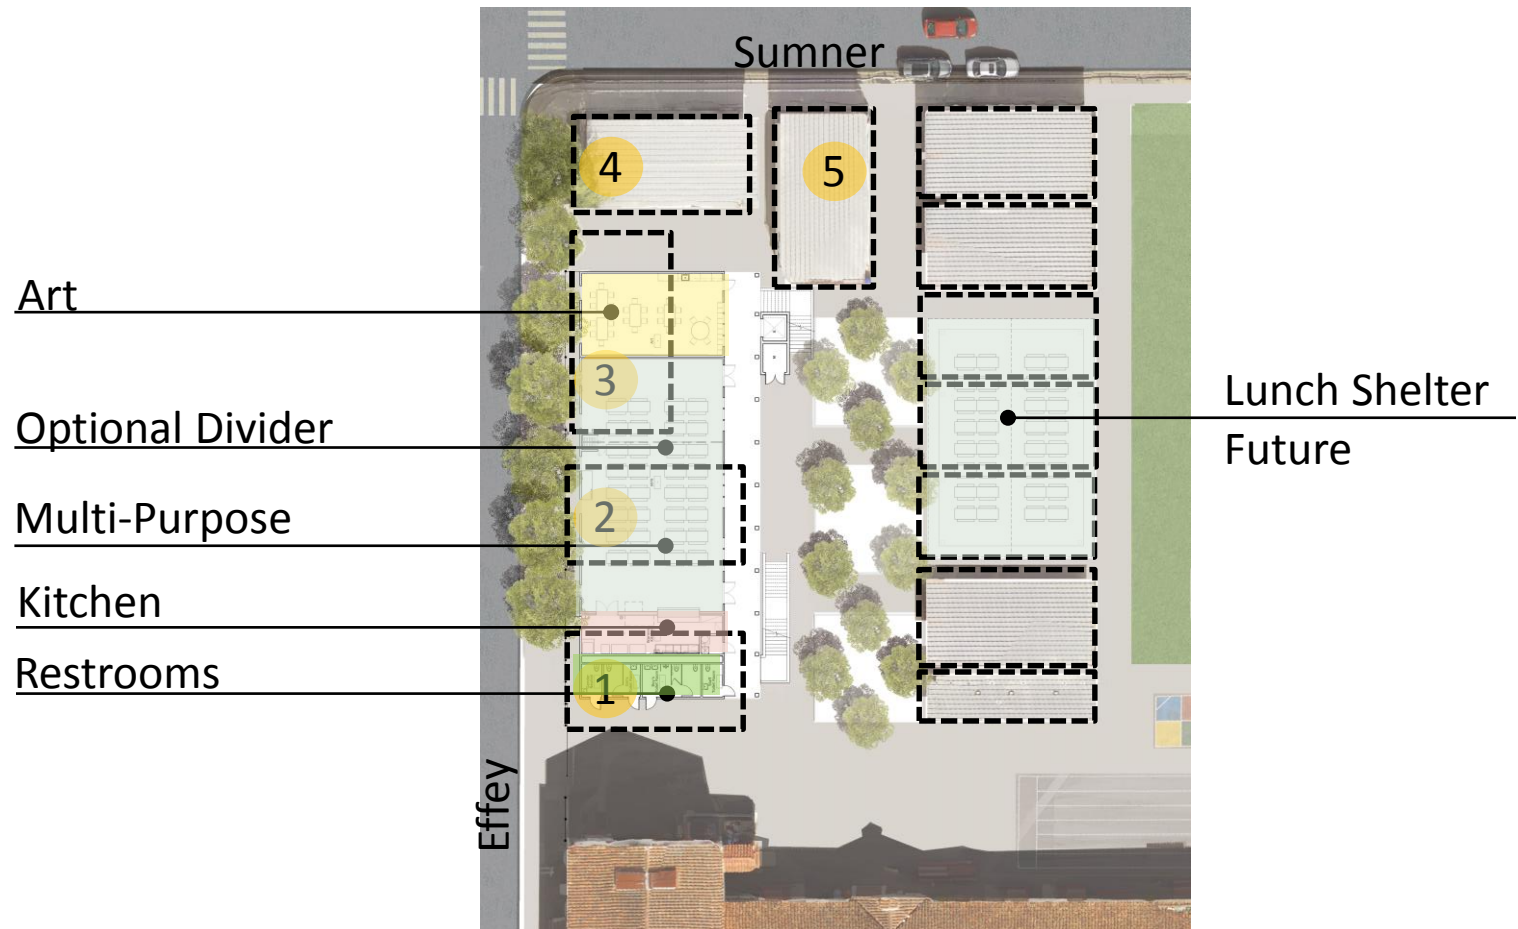

First Floor

Gault Elementary School: Masterplan

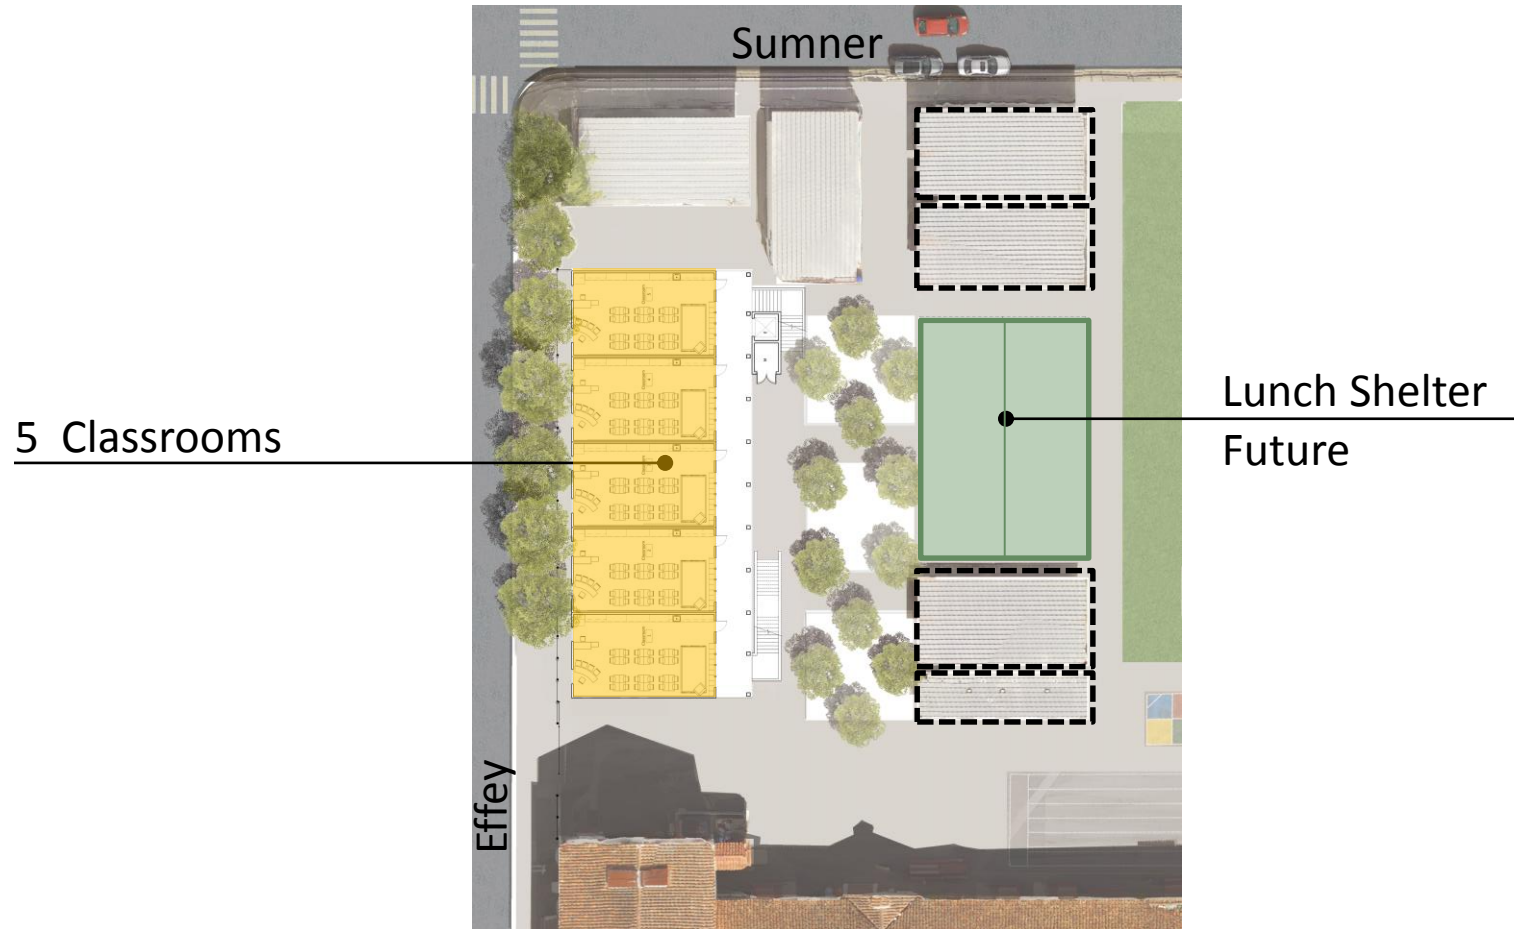

Second Floor
