

Measure A|B Update

Program Budgets and Expenditure Summary




SANTA CRUZ CITY SCHOOLS | BOARD MEETING – 16 SEPTEMBER 2021

Draft

Measure A | B Update

Expenditures

Program Snapshot	Resource	Expenditures To 06/30/21	Remaining Resource
Measure A: High Schools	\$140,000,000	\$88,063,491	\$51,936,509
Measure B: Elementary Schools	\$68,000,000	\$44,828,365	\$23,171,635
Measure A B Summary	\$208,000,000	\$132,891,855	\$75,108,145

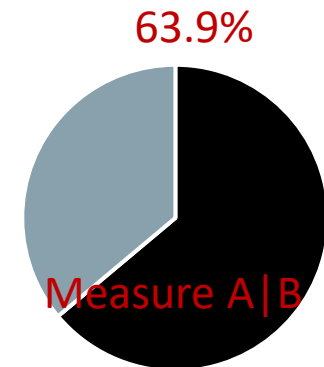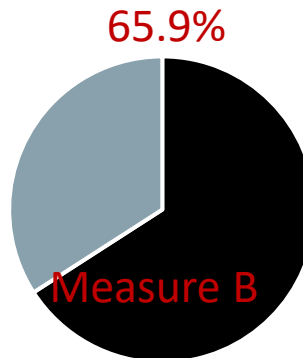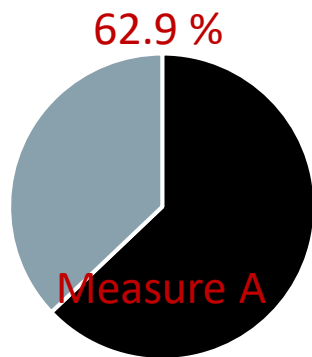

The values indicated here are based upon the Bartos Architecture program management database and indicate total expenditures throughout the program.

These values are periodically reconciled with District records.


Draft

Measure A | B Update

Terminology

- A Resource:** Funds available to site (including bond and state funds)
- B Allocation:** Budgetary allocation based on latest cost estimate, and prioritizations with site teams
- C Expenditure to Date:** Expenditures for a given project from November 2016 thru June 2021.
- D Percent Complete:** Proportion of amount actually expended divided by the total site resource.
- E Multi Project Overhead:** 5% of site resource for efforts not related to a specific project.
- F Utility Infrastructure:** Site (outside of buildings) utilities. Drainage, Gas, Water, Electrical.

D % Complete



A Current Resource \$xx,xxx,xxx

B Allocation

Expenditures

C To Date

E Multi Project Overhead

Project xyz

Project xyz

F Utility Infrastructure

\$

\$

\$

\$

\$ Total

\$

\$

\$

\$


\$ Total

Allocated so far

Draft

Branciforte MS Current Resource \$17,816,427

	Allocation	Expenditures To 06/30/21
Multi Project	\$200,000	\$133,218
Parking Lot Improvements	\$204,691	\$204,691
Re-Roof	\$1,678,923	\$1,678,923
Street Presence	\$1,850,000	\$1,500,961
Music/MPR	\$2,794,318	\$2,490,782
Library/Admin	\$2,700,000	\$198,041
Classroom Mod Phase 1	\$3,000,000	\$617,109
Relocatable Removal	\$900	\$900
Utility Infrastructure	\$9,245	\$9,245
Card Access Security System	\$182,110	\$182,110
Data Infrastructure Improvements	\$423,972	\$423,972
<i>Allocated so far</i>	\$13,044,160	\$7,439,952



42 % (Total Expenditures to 30 June 2021)

Draft

Measure A | B Update


High School Projects Expenditures

Mission Hill Middle School Current Site Resource \$18,399,904

	Allocation	Expenditures To 06/30/21
Multi-Project Overhead	\$952,206	\$144,128
Front Lawn (Hardscape Landscape)	\$1,299,864	\$1,299,864
Roof Replacement Phase 1	\$1,636,570	\$1,636,570
Roof Replacement Phase 2	\$750,000	\$166,364
Mod Phase 1 (Permanent walls)	\$647,648	\$647,648
Mod Phase 2 (Main Building)	\$300,000	\$24,085
Mod Phase 3 (Envelope)	\$1,334,468	\$25,600
New Classroom Building	\$6,424,679	\$6,766
Gym Locker Rooms Phase 1	\$188,536	\$188,536
Gym Phase 2 (Improve)	\$9,548	\$9,548
Site Improvements (incl Fencing)	\$269,276	\$67,343
Utility Infrastructure (incl. Power)	\$1,000,000	\$542,292
Card Access Security System	\$182,277	\$182,277
Data Infrastructure Improvements	\$401,086	\$401,086
Artificial Field Replacement	\$3,000,000	\$2,181,330
	<i>Allocated so far</i>	
	\$18,396,158	\$7,523,435

41 % (Total Expenditures to 30 June 2021)


Draft



Measure A | B Update

High School Projects Expenditures

Harbor High School	Current Resource	\$29,757,368	Expenditures To 06/30/21
	Allocation		
Athletic Field Improvements	\$11,904,433		\$11,904,433
Pool	\$10,676,597		\$10,676,597
Re-roof	\$2,237,734		\$2,237,734
Student Locker Improvements	\$257,067		\$257,067
Tennis Court Remodel	\$181,444		\$181,444
New Electrical	\$110,971		\$110,971
Student Restroom Hand Dryers	\$185,790		\$185,790
Data Infrastructure Improvements	\$910,542		\$ 910,542
Upper Parking Lot/Drop Off	\$21,806		\$21,806
Site Infrastructure	\$29,141		\$29,141
External Security	\$143,175		\$143,175
Mod 1: Fine Arts	\$320,000		\$86,080
Mod 2: Fine Arts	\$546,343		\$546,343
Card Access Security System	\$423,513		\$340,827
Multi Project	\$83,962		\$83,962
	<i>Allocated so far</i>	\$28,032,518	\$27,715,912



93% (Total Expenditures to 30 June 2021)

Draft

Measure A | B Update

High School Projects Expenditures


Santa Cruz HS	Current Resource	\$33,421,066	Expenditures To 06/30/21
		Allocation	
Multi Project Overhead		\$500,000	\$167,342
Mod Phase 1: (water line leaks)		\$778,872	\$778,872
Mod Phase 2: (Cafeteria, restroom, classes)		\$7,000,000	\$1,016,821
Mod Phase 3: (Math, Sci, Library)		\$1,750,000	\$151,001
Mod Phase 4: (Main building)		\$3,750,000	\$278,587
CTE Mod Transportation 1-Art Class		\$206,537	\$206,537
Gym Mod Phase 1: (Finishes, HVAC, Misc)		\$1,435,574	\$1,144,824
Gym Mod Phase 2: (lobby/fitness)		\$5,000,000	\$269,851
New Pool House (restrooms)		\$3,190,477	\$91,901
Fields		\$1,437,464	\$1,437,464
Sports Complex Upgrades		\$375,503	\$375,503
Re-Roof Phase 1		\$2,233,491	\$2,233,491
Re-Roof Phase 2		\$443,216	\$443,216
Card Access Security System		\$500,000	\$343,169
Data Infrastructure Improvements		\$1,455,735	\$1,455,735
Exterior Site Security		\$200,000	\$155,712
Campus Switchgear		\$2,581,994	\$931,133
Utility Infrastructure		\$282,223	\$282,223
		\$33,121,087	\$11,764,381

Allocated so far

35 % (Total Expenditures to 30 June 2021)

Draft

BARTOS
ARCHITECTURE




Measure A | B Update

High School Projects Expenditures

Soquel High School Current Resource \$36,297,747

	Allocation	Expenditures To 06/30/21
Multi Project	\$362,881	\$65,023
Site Infrastructure (safety/utilities)	\$3,749,473	\$3,730,713
New Snack Shack	\$1,874,151	\$1,840,391
Tennis Courts	\$201,100	\$201,100
Mod Phase 1:Reverse Tenant Improvement	\$1,927,766	\$1,927,766
Mod Phase 2: Wing 100, 200	\$12,532,383	\$12,531,996
Mod Phase 3: Other Special Areas	\$1,505,784	\$1,505,784
Pool	\$7,420,998	\$7,420,998
Fields	\$1,527,272	\$1,527,272
Card Access Security System	\$308,646	\$308,646
Interim Housing	\$118,542	\$118,542
Data Infrastructure Improvements	\$911,925	\$911,925
External Site Security	\$250,000	\$93,894
Performing Arts Center	\$161,113	\$61,303
	<i>Allocated so far</i>	
	\$32,852,034	\$32,245,351



89 %(Total Expenditures to 30 June 2021)

16 September 2021


collaboration | advocacy | research | education | sustainability

Draft

BARTOS
ARCHITECTURE

Bayview ES Current Resource \$13,252,496

	Allocation	Expenditures To 06/30/21
Multi-Project	\$69,546	\$69,546
Re-Roof	\$925,529	\$925,529
New WPENS Portable & Sitework	\$79,582	\$79,582
New Kindergarten Bldg & Sitework	\$92,477	\$92,477
New Classroom Bldg & Sitework	\$4,269,873	\$3,584,866
Modernization Phase 1	\$6,516,188	\$6,516,188
Modernization Phase 2	\$225,518	\$4,300
Portable Demolition & Site Work	\$10,250	\$10,250
Utility Infrastructure	\$50,825	\$50,825
Card Access Security System	\$190,000	\$164,415
Data Infrastructure Improvements	\$730,962	\$730,962
	\$13,160,749	\$12,228,939

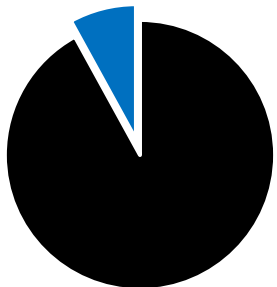


92% (Total Expenditures to 30 June 2021)

Draft

DeLaveaga ES

Current Resource \$15,188,051

	Allocation	Expenditures To 06/30/21
Multi-Project Overhead	\$43,154	\$43,154
New Parking Lot	\$1,542,166	\$1,542,166
New Classrooms	\$4,689,309	\$3,559,127
Re-Roofing Project	\$32,994	\$26,395
Mod Phase 1 (Classrooms)	\$7,300,568	\$7,300,568
Mod Phase 2 (Special spaces)	\$339,500	\$339,500
Portable Demolition & Site Work	\$100,000	\$36,902
Site Infrastructure	\$54,368	\$54,368
Card Access Security System	\$164,560	\$164,560
Data Infrastructure Improvements	\$846,345	\$846,345
	<i>Allocated so far</i>	
	\$15,112,965	\$13,913,087

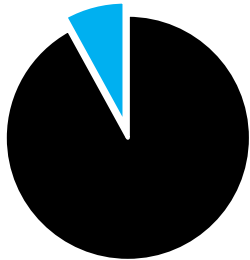


92 % (Total Expenditures to 30 June 2021)

Draft

Gault ES

Current Resource \$9,875,138

	Allocation	Expenditures To 06/30/21
Multi Project Overhead	\$425,000	\$122,503
Roofing	\$842,599	\$842,599
Modular Building	\$6,898,817	\$137,731
Mod Phase 1 Main Building (Water Intrusion)	\$117,184	\$117,184
Mod Phase 2 Main Building (Carpet)	\$100,000	\$0
Mod Phase 3 : Envelope (paint)	\$280,389	\$280,389
Utility Infrastructure	\$58,548	\$58,548
Card Access Security System	\$106,815	\$106,815
Data Infrastructure Improvements	\$466,316	\$466,316
<i>Allocated so far</i>	\$9,295,667	\$2,132,084

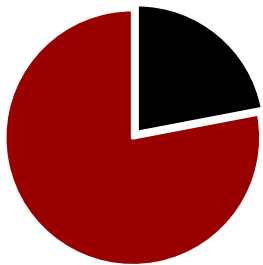


22 % (Total Expenditures to 30 June 2021)

Draft

Natural Bridges Current Resource \$4,267,937

	Allocation	Expenditures To 06/30/21
Multi-Project	\$5,570	\$5,570
Campus Re-Roofing	\$1,537,051	\$1,537,051
Gym Mod Ph 1 w/ Parking Lot	\$774,321	\$774,321
Gym Mod Ph 2 w/ Restroom	\$1,193,342	\$1,193,342
Modernization and Repairs	\$651,593	\$651,593
Artificial Field	\$106,061	\$106,061
<i>Allocated so far</i>	\$4,267,937	\$4,267,937




100 % (Total Expenditures to 30 June 2021)

Draft

Westlake ES Current Resource \$14,382,633

	Allocation	Expenditures To 06/30/21
Multi-Project Overhead	\$500,000	\$132,463
Re-roof	\$2,251,670	\$2,251,670
New Upper Classroom	\$4,750,000	\$40,690
Mod Phase 1: Upper Wing	\$1,000,000	\$130,692
Mod Phase 2: Lower Wing	\$1,000,000	\$109,130
Mod Phase 3: Main Building	\$21,692	\$21,692
Site Improvements, Sign, Fence, Access	\$1,001,981	\$581,312
Utility Infrastructure (incl power)	\$1,000,000	\$308,873
Card Access Security System	\$212,363	\$147,797
Data Infrastructure Improvements	\$961,585	\$961,585
Lower Parking and Drive	\$1,000,000	\$43,017
<i>Allocated so far</i>	\$13,699,290	\$4,278,930

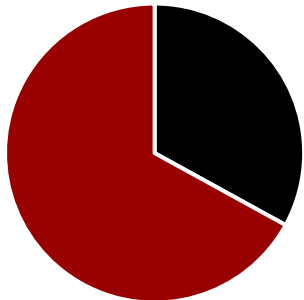


33% (Total Expenditures to 30 June 2021)

Draft

Branciforte Small Schools Current Resource \$9,184,764

	Allocation	Expenditures To 06/30/21
Multi-Project	\$24,950	\$22,907
Relocate Playground and Lunch Shelter	\$570,685	\$566,740
PC Classroom	\$4,421,635	\$3,282,447
Alternative Family Ed Campus	\$1,856,865	\$1,666,172
Mod Phase 1	\$1,540,549	\$511,813
Site Infrastructure	\$10,366	\$10,366
Card Access Security System	\$132,924	\$132,924
Data Infrastructure Improvements	\$681,016	\$681,016
	\$9,038,991	\$6,874,387



75%(Total Expenditures to 30 June 2021)

Draft

END

Draft
